

Dunkettle Progress Update

5th February 2021

[More Information at www.Dunkettle.ie](http://www.Dunkettle.ie)



[Twitter](#)



[Website](#)

Dunkettle Interchange Upgrade Project

Upgrade Dunkettle to a largely free-flow interchange to alleviate traffic congestion.

- Works between the N25 westbound lanes and the Viatrix premises should reach substantial completion over the next week or 10 days. See photograph below.




Installation of precast concrete protective slabs for gas transmission main nearing completion

- The M8 southbound will be reduced to one lane from the morning of Friday 5th February 2021 until Sunday 7th February 2021. The lane restrictions are being implemented during off peak hours in order to minimise disruption to traffic flow and the works are required to facilitate piling works on the new railway bridge to be constructed in this area. See photograph below.



Preliminary works advancing in the area of the new rail overbridge structure (ST08 on the layout plan attached). Initial piling works will be progressed here over this weekend.

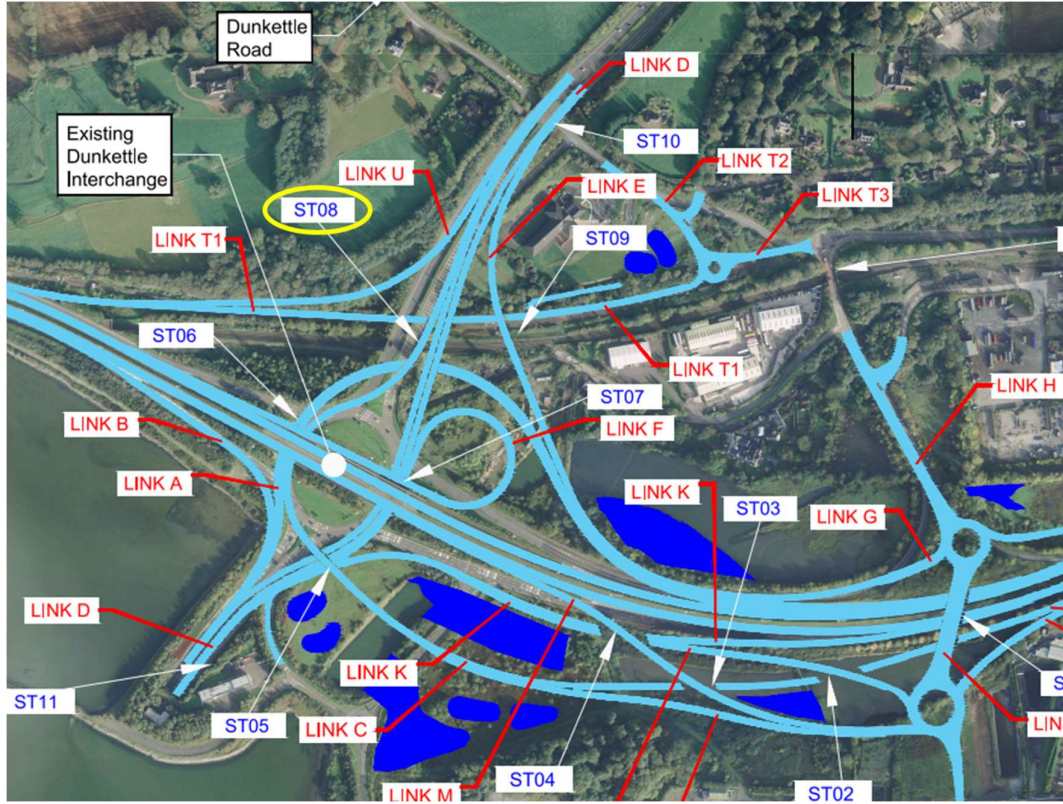


- Ground investigation works are also continuing throughout the site and these will continue well into February 2021. See photograph below.



Borehole being installed in order to determine ground conditions at depth for the Dunkettle Interchange Upgrade Scheme

- No significant disruption to traffic is anticipated over the coming week.



N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

- Duct installation works will continue under lane 2 ("fast" lane) over the coming days. Works in this area are being progressed on a 24 hour basis and we hope to reach completion by next weekend, Saturday 13th February 2021. See photograph below.



Duct installation works on the N8 at Tivoli

- The hard shoulder closure on the N40 eastbound between Mahon Interchange and the Jack Lynch Tunnel will remain in place for a number of weeks. Works are ongoing on 3 sites within this area. See photographs below.



Reinforced concrete piles installed for gantry foundation



Piling works getting underway for a further site on the N40 eastbound again with a view to installing reinforced concrete piles to provide a gantry foundation

- Works will also continue on the N25 westbound in the Little Island Interchange area for a number of weeks.

Contact Us

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
