
## Dunkettle Progress Update 21st January 2022

More Information at www.Dunkettle.ie





## Dunkettle Interchange Upgrade Project

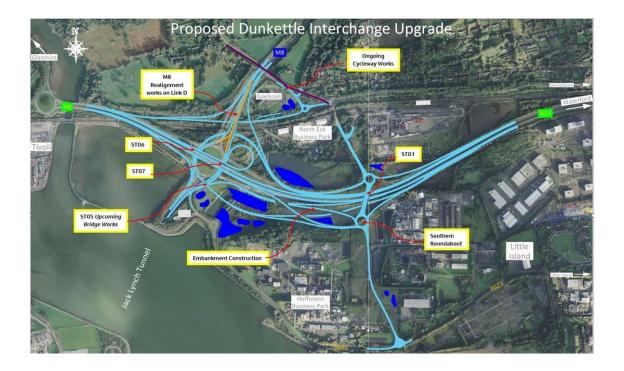

 Embankment construction for proposed links K, L, M, P and for the Southern roundabout of the new eastern interchange will continue over the coming months- see photograph below.



Embankment construction ongoing south of the N25.

- Column construction works at Structure St05 will be getting underway over the coming days in the area immediately adjacent to the Southbound approach to the Tunnel.
- Traffic management arrangements associated with opening of Structure St 08 and with permanent opening of the first link roads of the new alignment to come into service are currently being finalised. Details will be set out in an additional update on next

Monday 24th January.

 Bridge deck works will continue on structures St06 and St07 over the coming weeks- see photograph below.




Works ongoing at St06.

 Construction of the cycleway / walkway adjoining the Dunkettle local road are progressing well – see photograph below.




**Cycleway Works ongoing.** 

Please see hereunder link to recent drone footage showing the ongoing works on the deck of ST01:

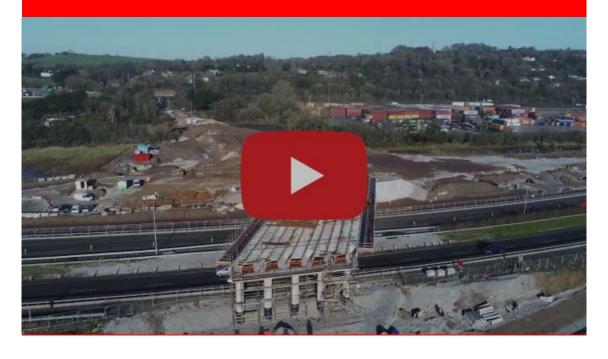

## **Dunkettle Live Traffic App**

Motorists are again reminded of the availability of the "Dunkettle
Live" traffic app. In addition to live camera feeds, real time journey
duration information is also available for all of the main routes
approaching the Dunkettle Interchange Roundabout.

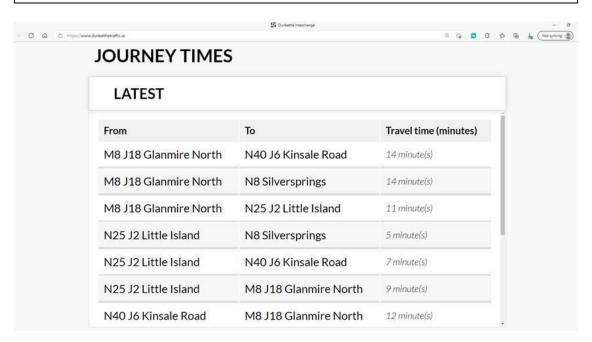

Click on the image above to see the benefits and features of the Dunkettle Traffic website.









Dunkettle Live App: Download from Apple App store or from Google Play store

## N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

Works in relation to the ongoing ITS works will continue as follows:

 Commissioning of the new Overheight Vehicle Detection System south of the Jack Lynch Tunnel Tunnel has continued over the past week. The photo below shows lane control signs under test where the detection of an overhead vehicle prompts the display of advisory speed limits on the approach to the tunnel.



Electronic Signage under test on eastbound N40 approach to Jack Lynch Tunnel.

- A tunnel closure is scheduled next week for the installation of large Variable Message Signs over both the north and south portals of the tunnel. This represents a significant upgrade of the safety infrastructure directly in advance of the Jack Lynch Tunnel.
- In order to minimise disruption to motorists, a large amount of other ITS works are scheduled to coincide with this closure, including the installation of traffic signals and Over-Height Vehicle Detectors (OHVDs) on the N40 approach to the tunnel.
- Electronic Variable Message Signs will also be installed on the new gantry between the Bloomfield and Mahon junctions over both the

eastbound and westbound carriageways, over Monday to Thursday nights next week. The works have been planned to avoid closure of the N40 carriageway at any stage but traffic will be reduced to one lane.

As always, if there are any queries or comments in relation to these works, please contact us at:

**Phone:** 1800 810077 (at any

time), Email: roadconstruction@ccc-site.com.

Acomhal Dhún Citil Dunkettle Interchange

Further information on the Dunkettle Scheme can be accessed <a href="https://www.dunkettle.ie">www.dunkettle.ie</a>.

Real time traffic information can be accessed via <a href="https://www.dunkettletraffic.ie">www.dunkettletraffic.ie</a> or on the Dunkettle Live App (Apple App store and Google Play store).

New subscribers to the newsletter can

register: www.dunkettle.ie/newslettersignup

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?
You can update your preferences or unsubscribe from this list.
