

# Dunkettle Interchange Upgrade Project



More at  
[www.Dunkettle.ie](http://www.Dunkettle.ie)




## Dunkettle Progress Update *25th March 2022*



Twitter



Website

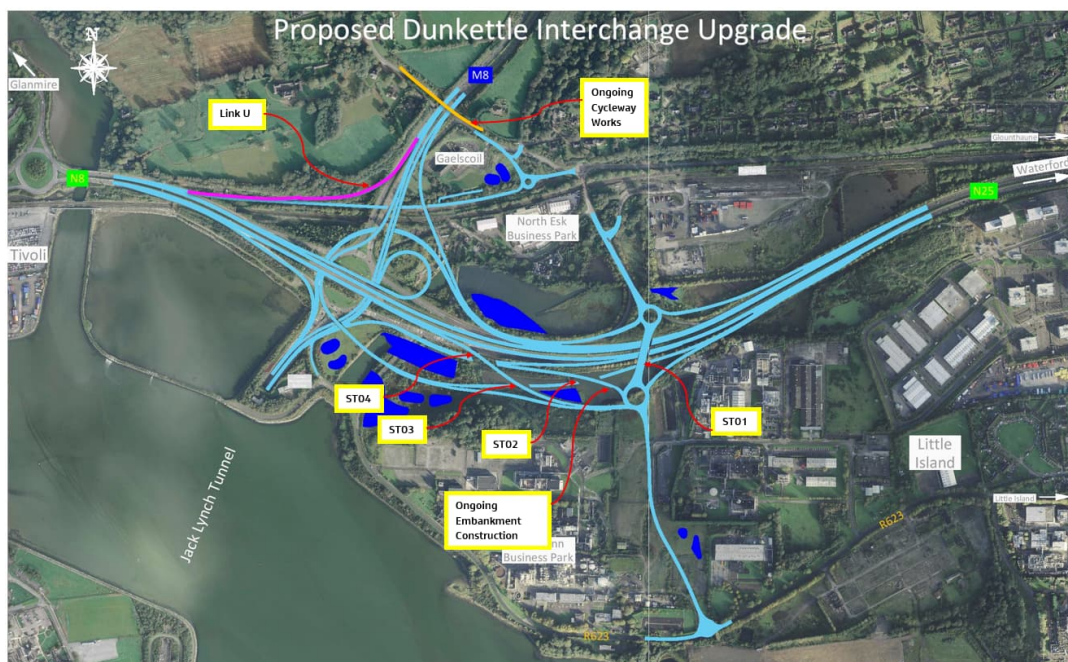

As part of our works we will be resurfacing the N25 from the Dunkettle Roundabout to the Little Island Interchange – preliminary works including installation of ducting and drainage systems will continue on the N25 (mainly under night time working) over the coming period.

Embankment construction will continue in the area south of the existing N25 for several months – see photograph below.



**Embankment Construction works ongoing alongside the N25 westbound**

As part of the works in this area, construction is now well underway at Structures 1-4 inclusive - see photograph below.



**Works ongoing at Structure 3 south of the N25.**

We still hope to open Link U to traffic during April 2022. However, we



are now proposing to take advantage of the reduced traffic volumes during the upcoming Easter school holiday period to facilitate these works. Preliminary works will get underway immediately under night time working. We then expect that lane restrictions will be in place for approximately 1 week from Friday 8th April 2022 to Saturday 16th April 2022. Further details will be provided in next weeks update – see photograph below.



**Pavement tie in works area for Link U to the N8/N25 eastbound .**

We still hope to complete the works on the cycleway on the L2998 between Burys Bridge and Dunkettle by the due completion date of May 2022 – see photograph below.



**Works ongoing for the new cycleway on the L2998, under the M8.**

In overall terms the works remain on track for completion by the due date of February 2024.

See video below indicating the ongoing works on the Link U northern tie-in with the M8.



## Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.





**Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)**

# N40 Intelligent Transport Systems

*Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.*

Commissioning of the Over-Height Vehicle Detectors (OHVD) on the approach to the tunnel is ongoing by night to minimise impact on road users.

Site Acceptance Testing of the full Over-Height Vehicle Detection System including Variable Message Signs and Barriers is scheduled to coincide with the night time Tunnel Maintenance closure from 11th to 14th April.



## Over-Height Vehicle Detectors (OHVDs) and supporting infrastructure on the M8 Southbound approach to Dunkettle.

As always, if there are any queries or comments in relation to these works, please contact us at:

**Phone:** 1800 810077 (at any time),

**Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).

Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



**More at**  
**[www.Dunkettle.ie](http://www.Dunkettle.ie)**



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).

This email was sent to <<Email address>>

[why did I get this?](#) [unsubscribe from this list](#) [update subscription preferences](#)

N40/Dunkettle Team · Tunnel Management Building · Dunkettle · Glanmire, CO. CORK T45 E898 · Ireland
