

Dunkettle Progress Update


23rd September 2022



Twitter




Website

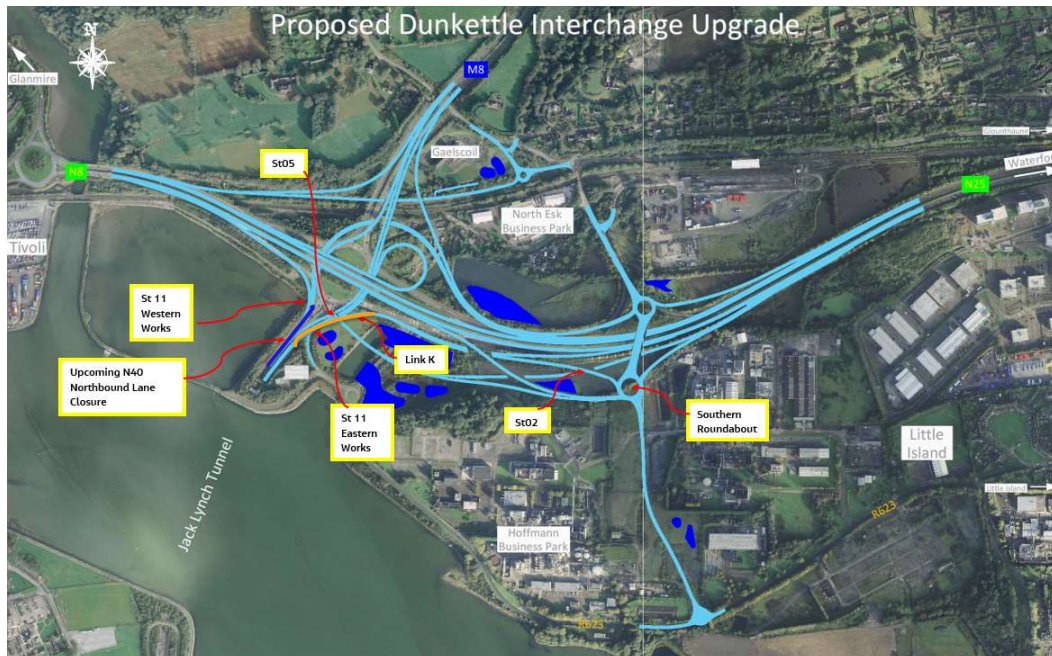

- Dunkettle Works are heading into a particularly busy phase over the coming period and motorists are again advised that speed control measures will be in place on approach to the site on a continuous basis.


- At present, there is a significant focus on the construction of the eastern section of Structure St11 and on the surfacing works on the southbound approach to the Jack Lynch Tunnel – see photograph below. These works will continue over the coming period with night-time working being progressed in order to minimise disruption to traffic as appropriate

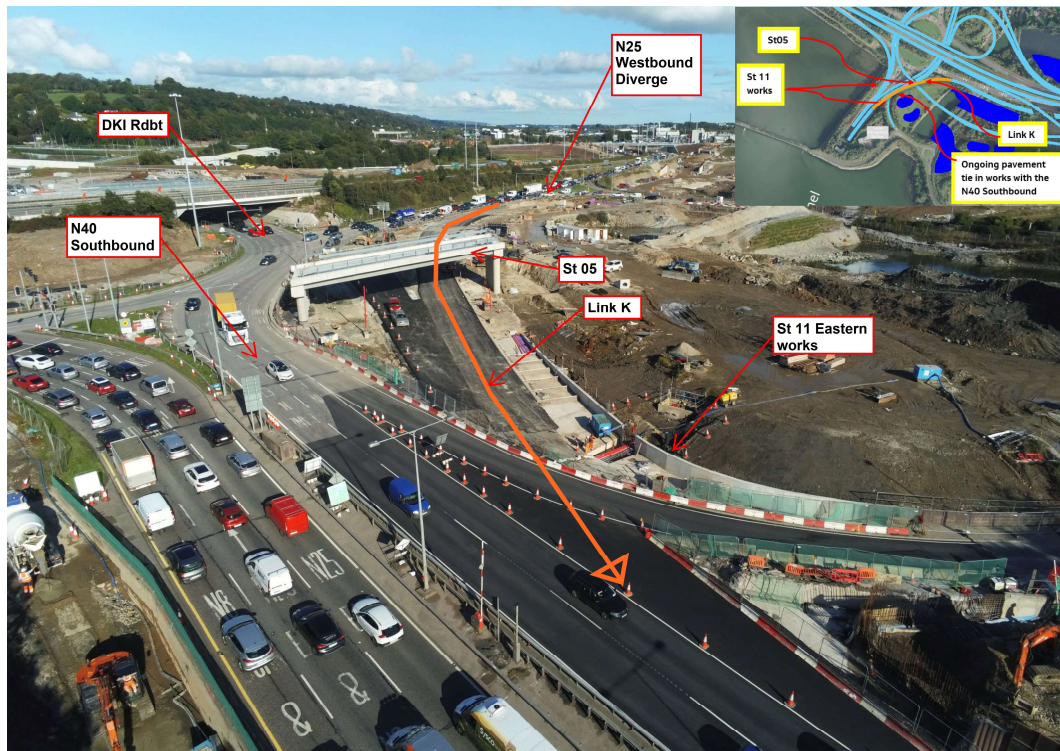

Works ongoing at St11 alongside the N40 southbound approach to the Jack Lynch Tunnel.


- Over the coming days, works will also recommence on the western section of Structure St11. Demolition of the existing boundary wall in this area will necessitate a temporary closure of a traffic lane on the northbound approach to the Interchange Roundabout - see photograph attached. We expect that this lane closure will be put in

place from Wednesday 28th / Thursday 29th September with the initial demolition works taking 3 or 4 days to complete. Motorists are advised to allow extra time for their journey, particularly during peak hours if using the northbound exit from the Jack Lynch Tunnel.

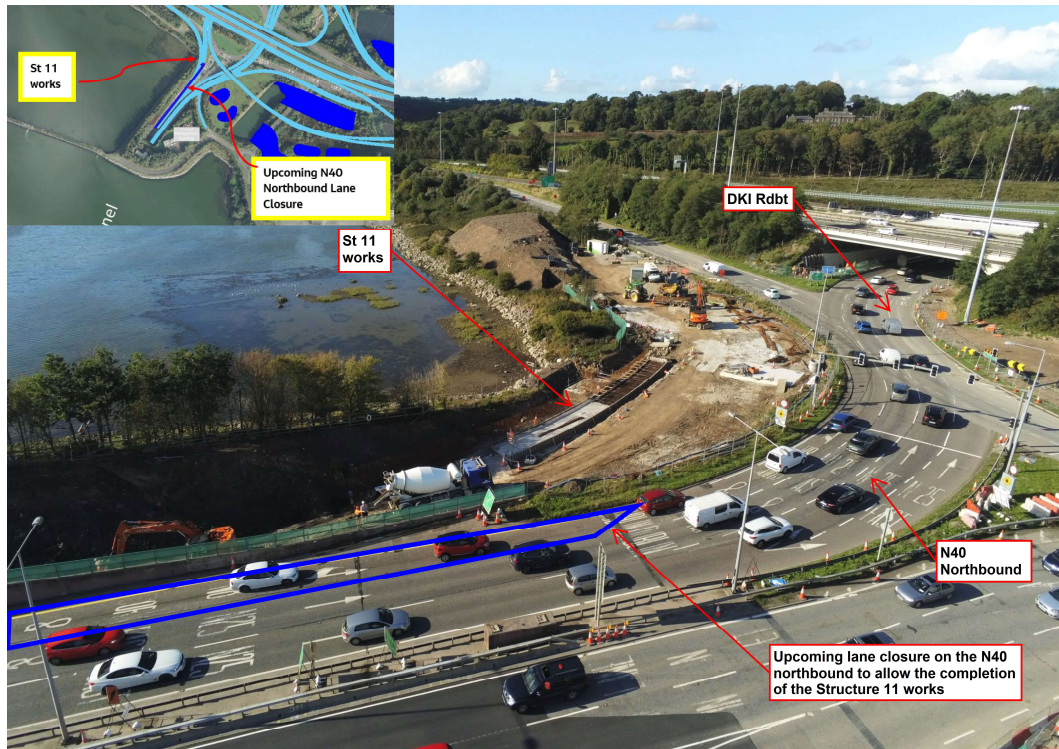

Preparatory works ongoing at the western side of the new St11 retaining walls alongside the N40 Northbound.

- In relation to bridge structures we hope to cast the deck of Structure St02 over the coming days – see aerial shot of the Structure attached.

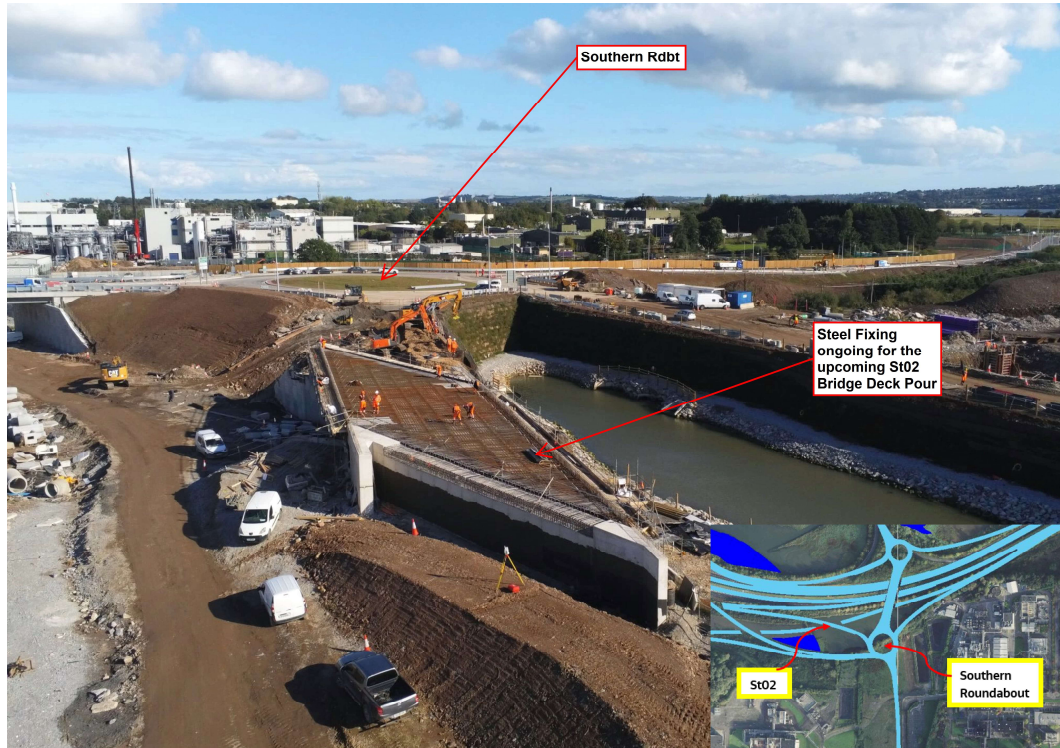

Steel Fixing works ongoing at Structure St02.

- In general, motorists will notice an increased focus on works in online areas and on works immediately adjacent to existing carriageways over the coming weeks. There will be a particular focus on surfacing works and the temporary lane closure at the northbound approach to the Interchange Roundabout will be followed by opening of a number of new road links during October 2022 – details of the upcoming link openings will be provided in next week's Progress Update.

**This weeks video shows the ongoing works on the southern side of
the N25 between Structure St04 and Structure St01.**



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:
Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
