

Dunkettle Progress Update


30th September 2022



Twitter



Website

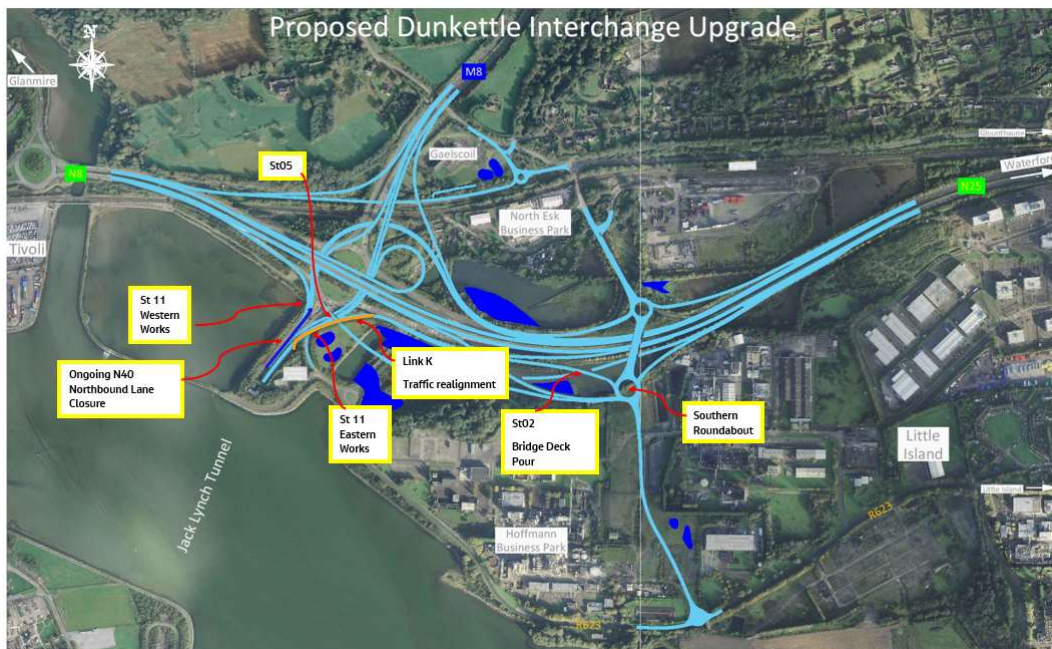

- Motorists are again reminded that speed control measures will be in place across the site on a continuous basis over the coming weeks.


- The configuration of the N25 westbound diverge approach (Link K) to the Dunkettle Interchange Roundabout will be adjusted over the coming period. The proposed new alignment in this area is shown on the layout plan attached. The existing traffic lights will be relocated to cater for the new alignment. The purpose of the adjustment in this area is to facilitate access for ground improvement works in the area immediately west of Structure St05, shown hatched on the layout plan attached.



Upcoming traffic realignment on the N25 westbound diverge approach to the DKI Roundabout.

- Traffic Management measures remain in place on the northbound lanes between the Jack Lynch Tunnel and the Interchange Roundabout. These are required to facilitate demolition of the

existing retaining wall at this location – see photograph below. These works are adding to delays at peak times and we propose to continue these works over the coming weekend with a view to minimising this disruption. The scope of the Traffic Management measures is being reduced as the works are progressed and we hope that these Traffic Management arrangements will be fully removed by Friday 14th October 2022.

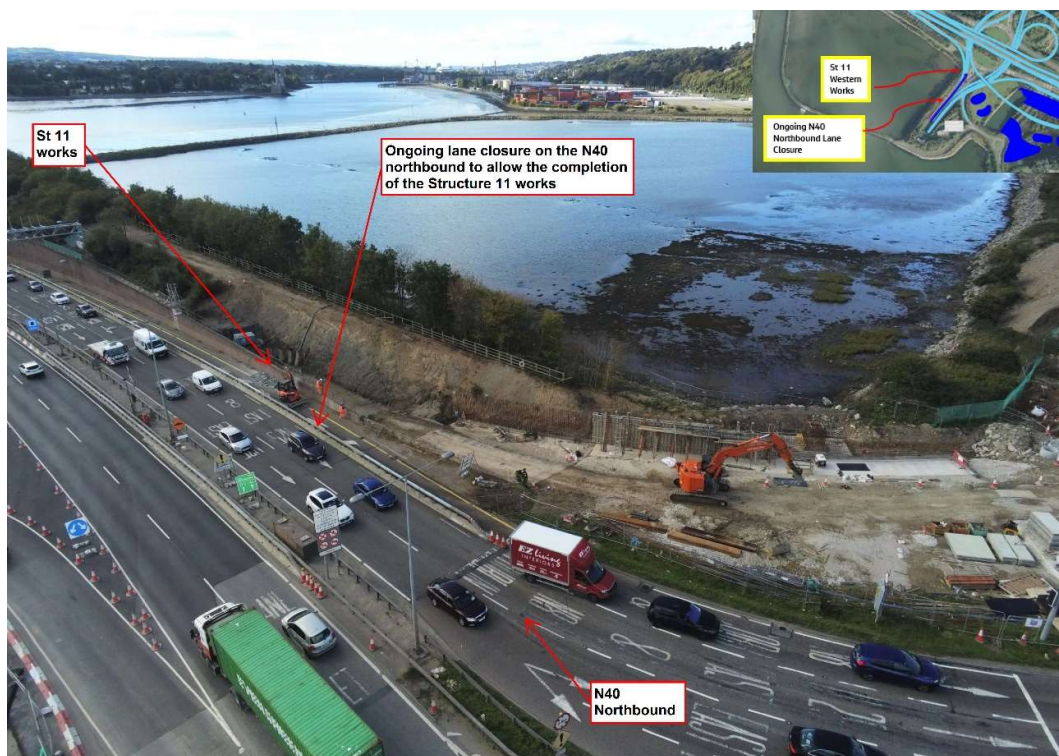

Ongoing works on the N40 northbound approach to the DKI Roundabout.

- In relation to Bridge Structures, the bridge deck of Structure St02 was cast as planned on Wednesday 28th September 2022 – see photograph below.



Completion of the St02 bridge deck works ongoing during the period.

- Motorists are requested to take particular care over the coming months while layout changes are implemented at various locations. The construction focus overall will continue to be on online areas and areas immediately adjacent to existing traffic lanes.

- In terms of the overall construction programme, the Dunkettle works remain well on track for completion by the due date of February 2024.

This week's video shows the ongoing works on Links T, H and Q. This shows the route which will form the new access from the N8 eastbound to R623 Roundabout in Little Island.



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)



As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.

Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
