

Dunkettle Progress Update


24th February 2023



[Twitter](#)




[Website](#)

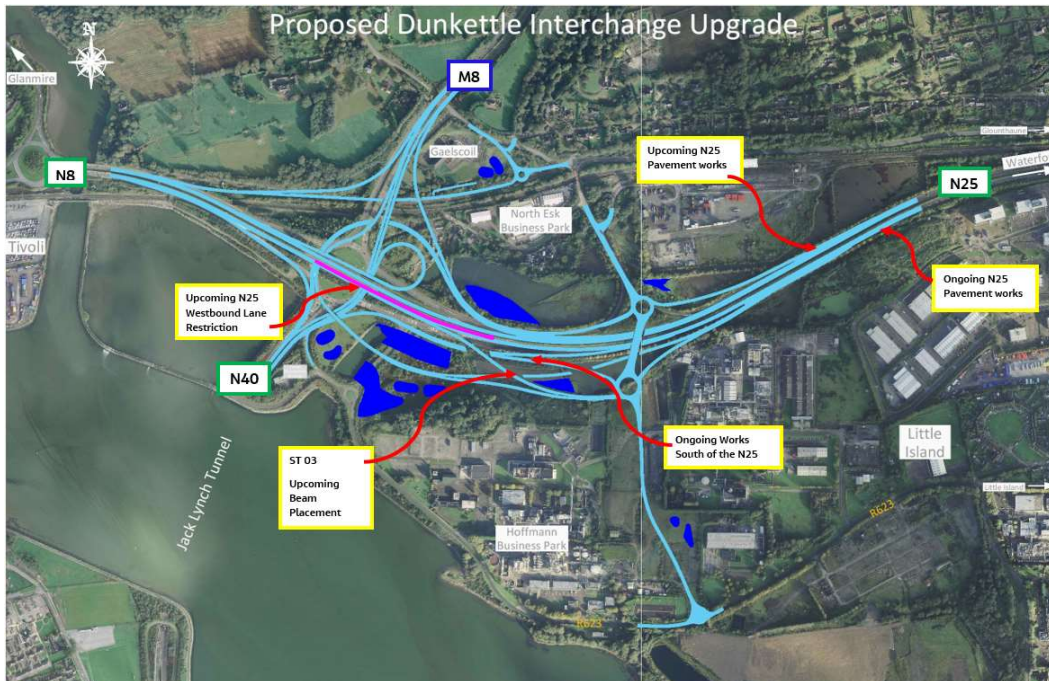


- Motorists are again reminded that speed control measures, coupled with CCTV monitoring are in place across the site and will remain in place over the coming months.

- The final set of beams on the project will be placed under daytime working on Tuesday 28th February 2023 – see photograph below. The starting time will be 5am approximately in order to ensure that the beams are brought to site in advance of the AM traffic peak. On completion of this work, a total of 135 beams will have been placed on the project.

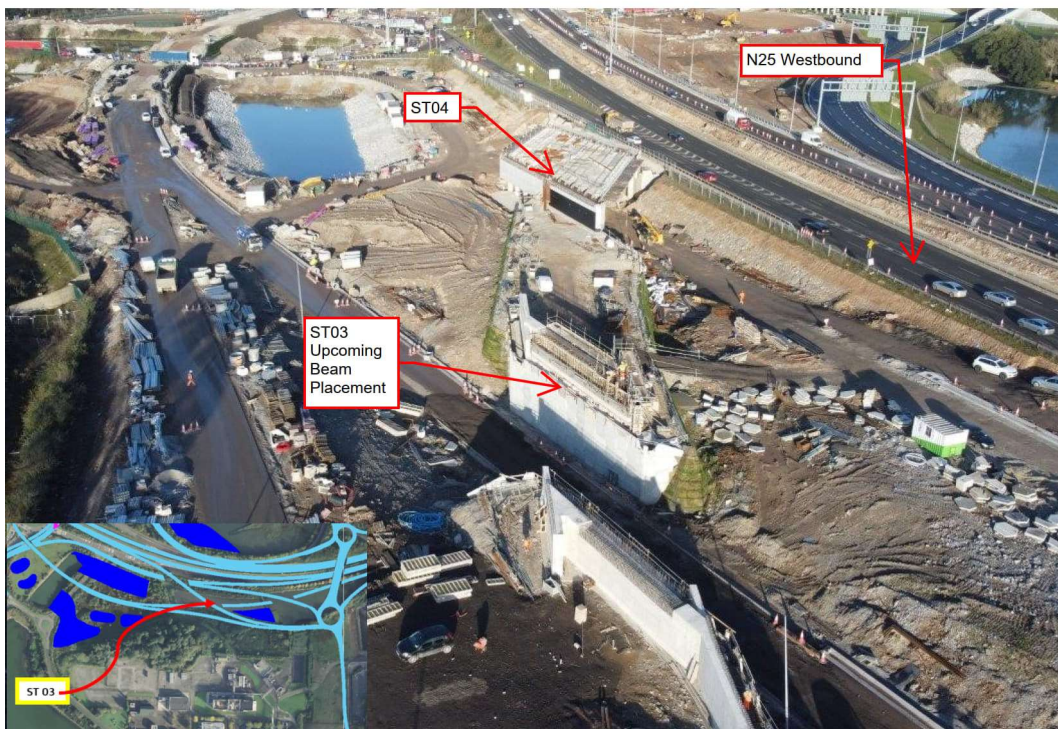

Works being undertaken at Structure ST03 in advance of the upcoming beam placement.

- Offline works are continuing on Links K, L, M and C - see photograph below.

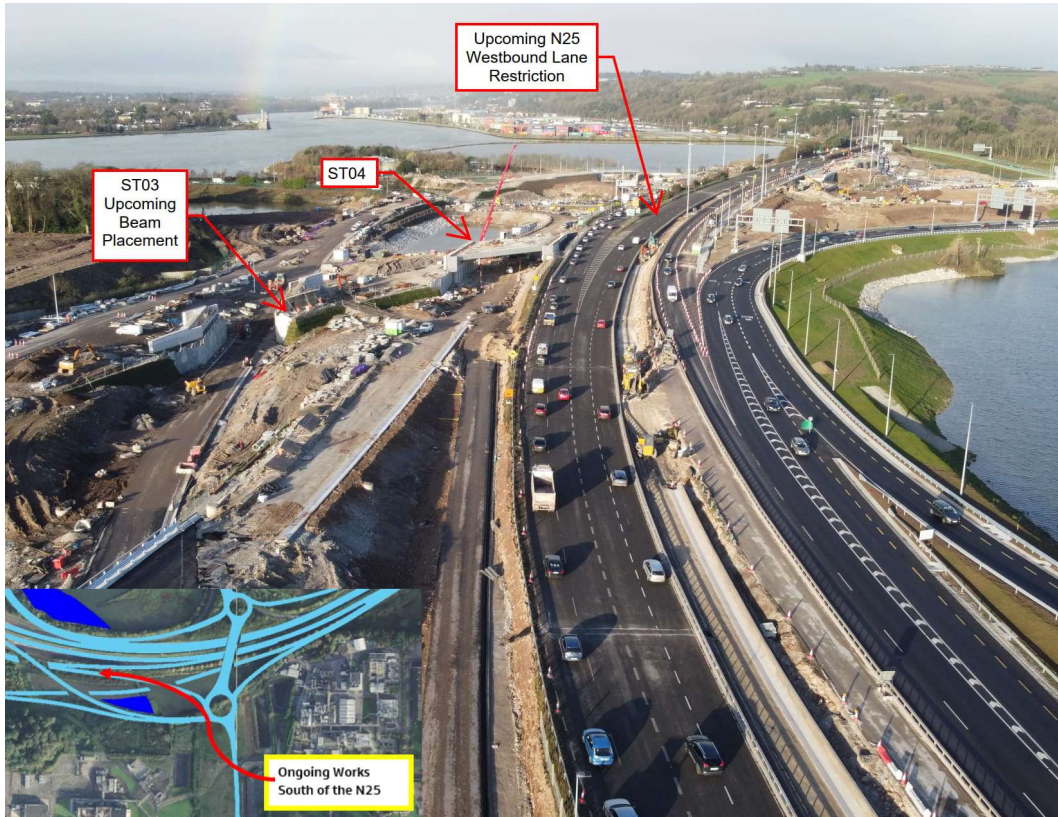


Works ongoing south of the N25 Westbound.

- Over the course of this week, we have completed the next section of surfacing works on the N25 Westbound. Lane relocations will be implemented here over the coming days to facilitate completion of works in the N25 central median west of Structure ST01 and on Link K south of the N25 – see and photograph below. N25 Westbound traffic heading to Tivoli roundabout will be reduced to one lane for a short section (see layout plan below) from W/C 27th February 2023 for several weeks. Two lanes will remain open for the diverge to the Interchange Roundabout and no traffic disruption is anticipated as a result of the same.




Pavement works being undertaken at night on the N25 Westbound.

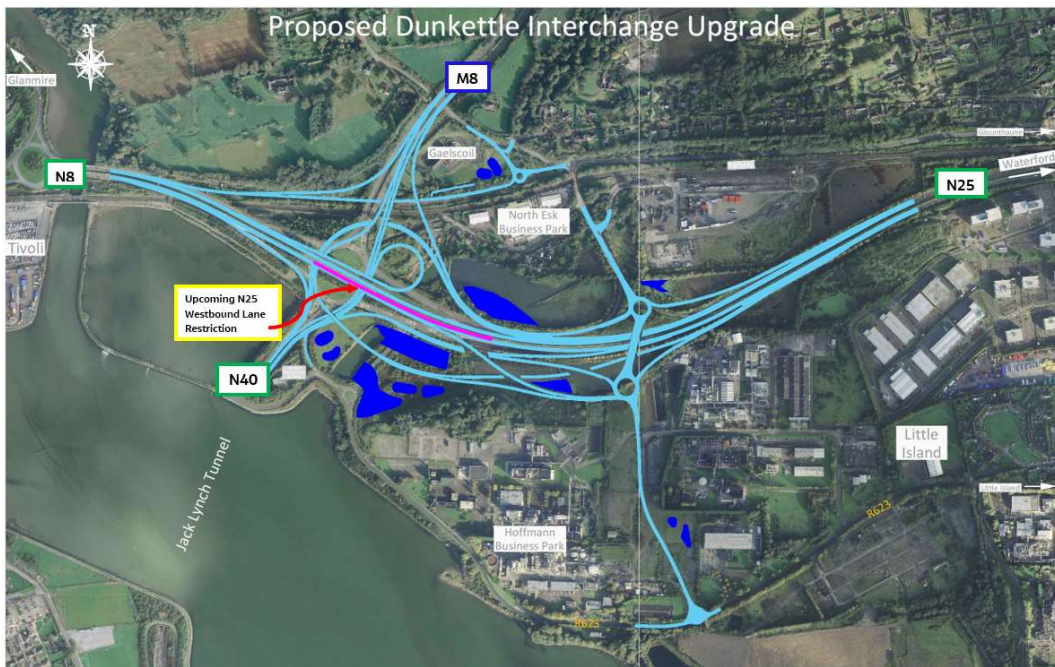


Location of the lane restriction for traffic heading to the Tivoli Roundabout.

- Over the coming week, the focus from a surfacing works point of view will be on the N25 Eastbound in the area east of Structure St01. Final surfacing will be laid from Structure St01 to the eastern tie-in. On completion of these works we intend to remove a section of the TM measures with all lanes permanently open - see photograph below.

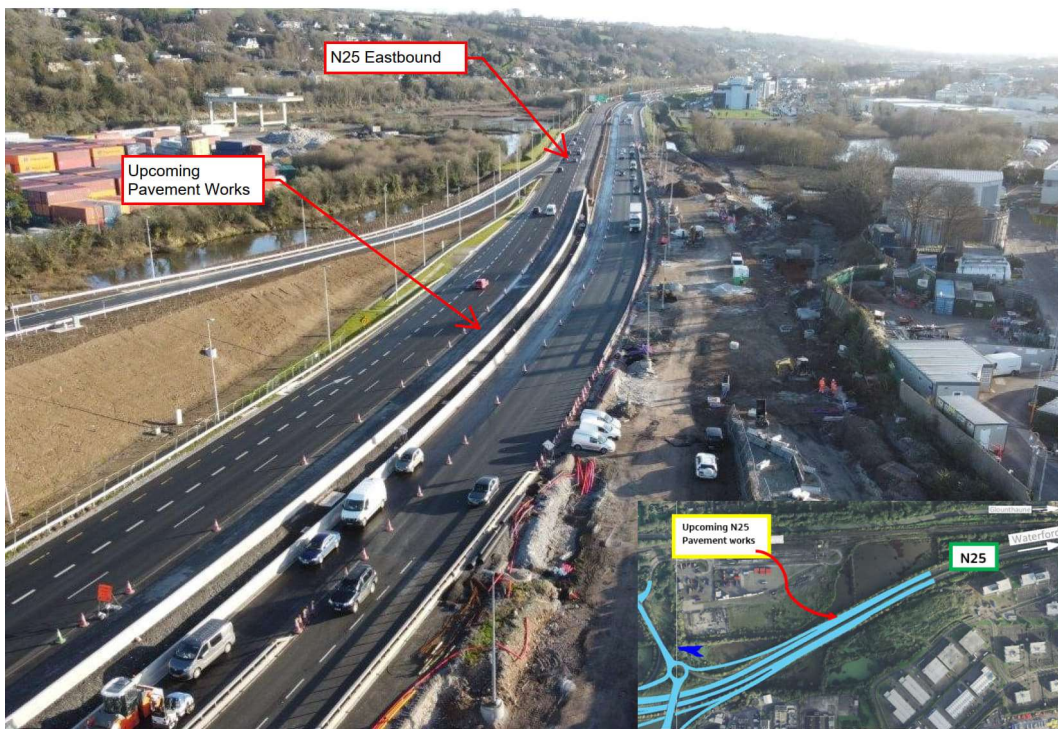

Upcoming pavement works on the N25 Eastbound.

This week's video shows the ongoing construction works on Link K which will ultimately form the new free flow link from the N25 Westbound to the Jack Lynch Tunnel.

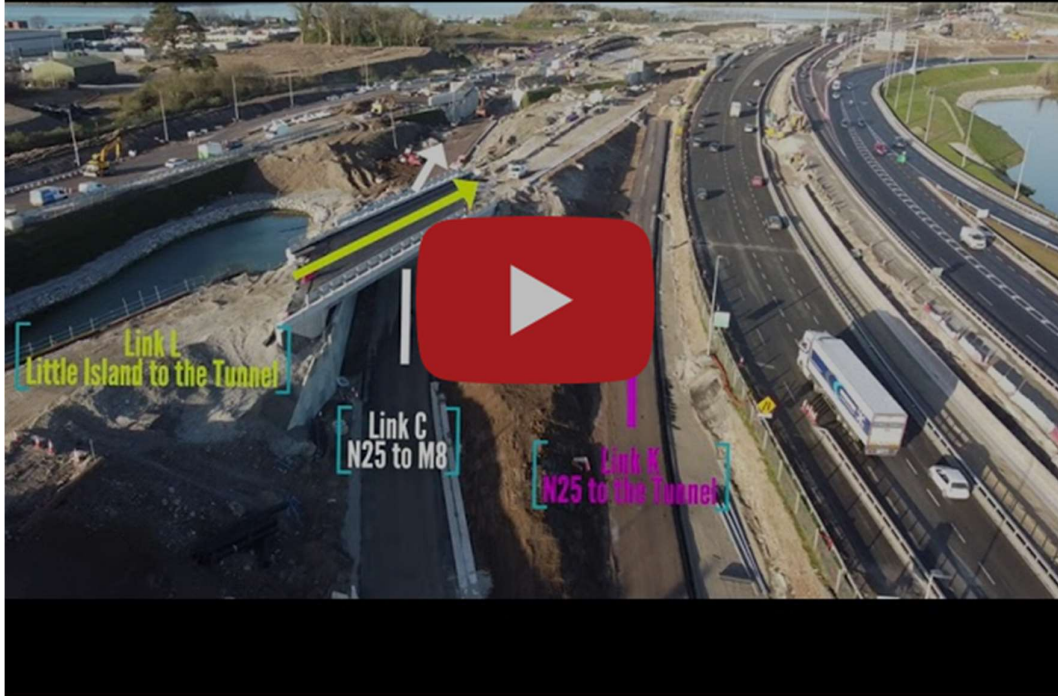

Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:
Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?
You can [update your preferences](#) or [unsubscribe from this list](#).
