

Dunkettle Progress Update


22nd September 2023



[Twitter](#)



[Website](#)

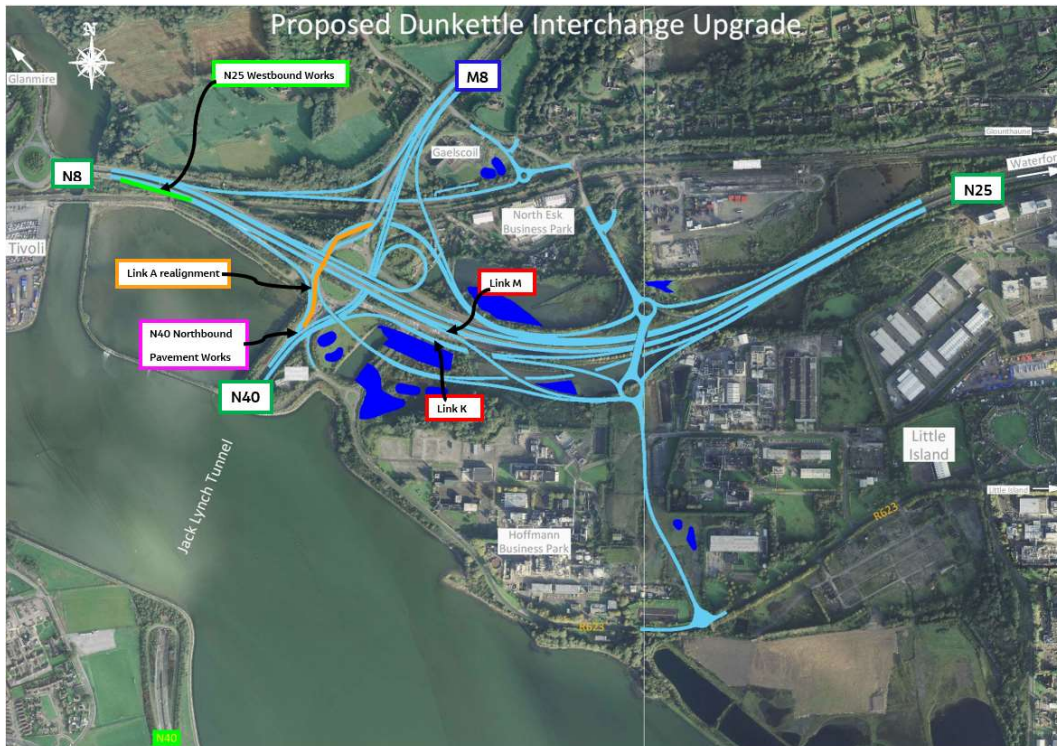


- Work is currently focused on the completion of the area north of the Jack Lynch Tunnel. N40 northbound traffic can now use both lanes through the Tunnel to access the N25 eastbound. Signage and lining works associated with the new arrangement are currently being completed under night time working as weather conditions allow – see photograph below.




Pavement works ongoing on the N40 northbound directly north of the Jack Lynch Tunnel

- N40 northbound traffic wishing to access the N25 eastbound has been temporarily switched to allow the permanent lanes for this N40 to N25 movement to be completed. The works area for this item is under the western interchange bridge. Works in this area will continue for a number of weeks - see photograph below.

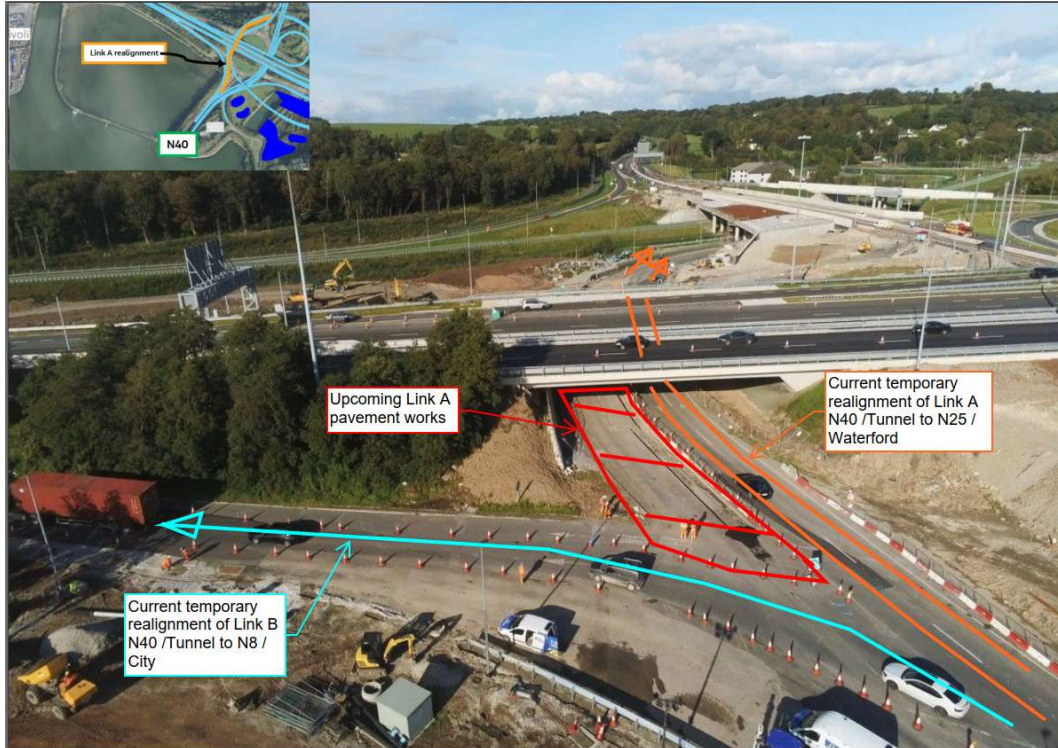


Current temporary lane configuration of the N40 traffic bound for the N25 Eastbound in the vicinity of the old Interchange Roundabout

- N40 northbound traffic wishing to access the M8 northbound should exit the N40 from the right hand lane. N40 Northbound traffic wishing to access the N8/N25 westbound should exit the N40 from the left hand lane – see photograph below.

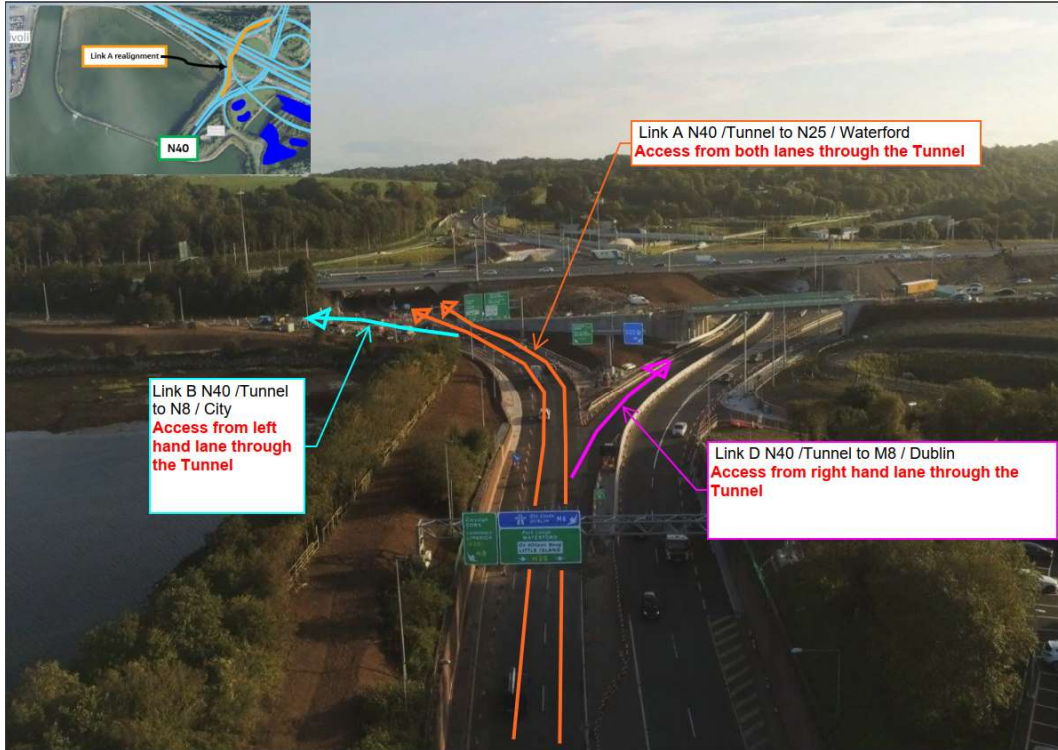


New lane configuration in place directly north of the Jack Lynch Tunnel

- Traffic on the N40 northbound can now use both lanes through the Jack Lynch Tunnel to access the N25 eastbound - see photograph below.

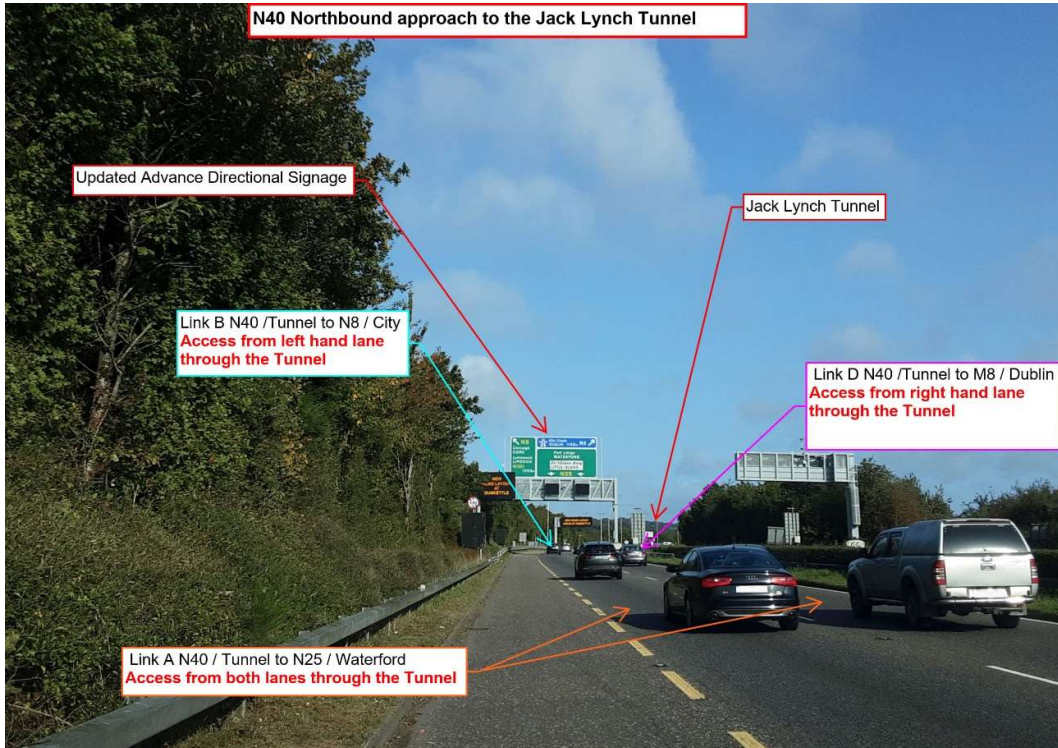


**New lane configuration in place directly south of the Jack Lynch Tunnel
on the N40 northbound**

- Weather conditions have slightly delayed the completion of the surfacing works on the N25 westbound approach to the Tivoli Roundabout. We now hope to complete these works under night time working early in W/C Monday 25th September 2023 – see photograph below.

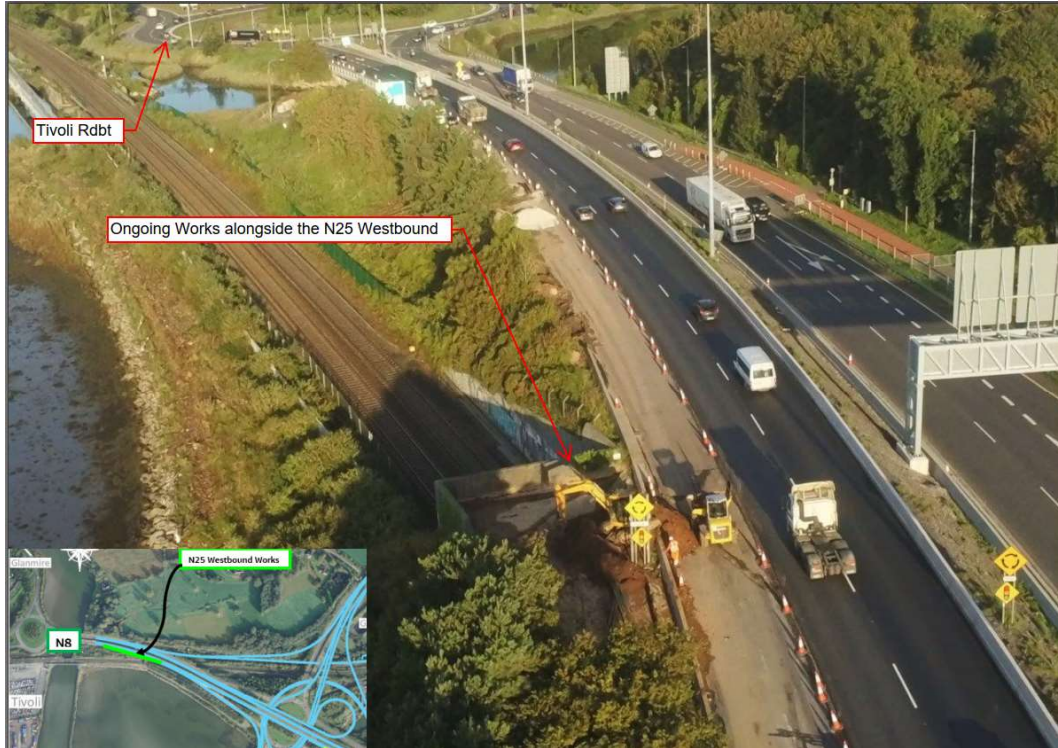


N25 Westbound upgrade works ongoing on the approach to the Tivoli Roundabout.

- Works will also continue on Links K & M (see layout plan and photograph below) over the coming period and this area should reach full completion during October 2023.

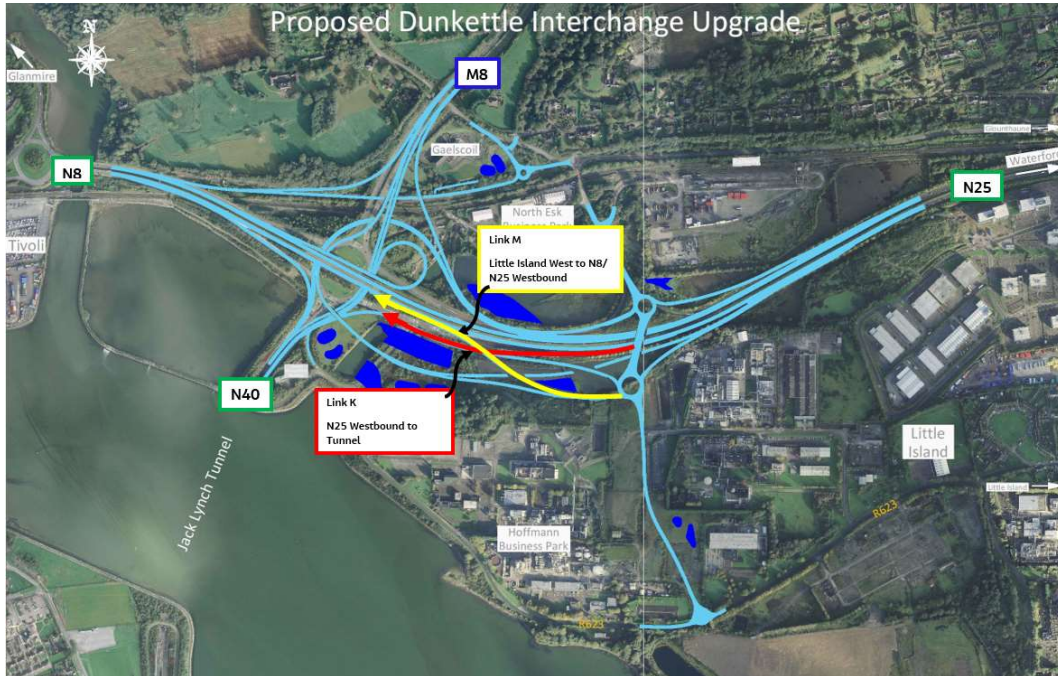


Link K & Link M Ongoing Works Location

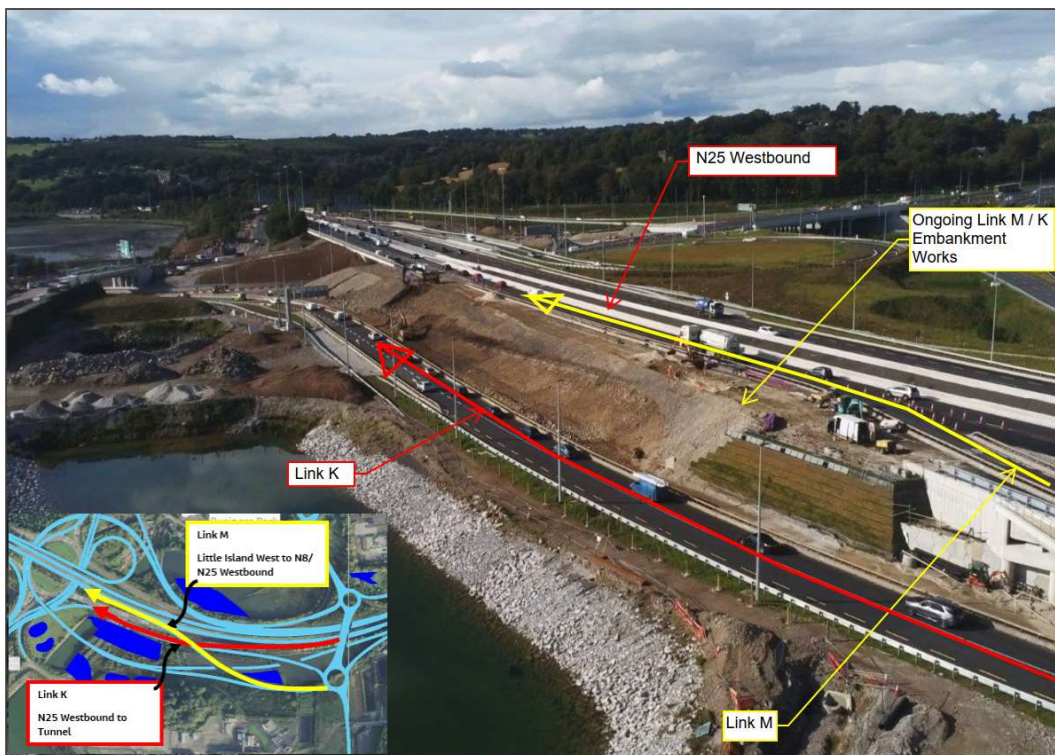

Link K & Link M Works ongoing alongside the N25 Westbound

This week's Progress Update video shows the ongoing works on the N40 northbound approach from the Jack Lynch Tunnel to the Dunkettle Interchange



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:
Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?
You can [update your preferences](#) or [unsubscribe from this list](#).
