

Dunkettle Progress Update

11th December 2020

[More Information at www.Dunkettle.ie](http://www.Dunkettle.ie)



Twitter



Website

Dunkettle Interchange Upgrade Project

Upgrade Dunkettle to a largely free-flow interchange to alleviate traffic congestion.

- Ground investigation works are continuing across the site. Night time lane restrictions will be in place on the Dunkettle Interchange Roundabout on the nights of Monday 14th and Tuesday 15th December 2020 to facilitate these ground investigation works in the Roundabout centre island. Works will be carried out between 10 pm and 5 am and no disruption to traffic is expected.
- Works are continuing on the gas transmission main protection slab in the area between the Upjohn premises and the N25 westbound

route. We now expect that these works will continue into January 2021.




Concrete being poured to form the support beam for the concrete protection slabs at the gas transmission main site

- Stockpiling of material in the area immediately north of the new roundabout on the R623 Little Island Regional Road is continuing. We now expect that approximately 30,000 tonnes of material will be placed in this area prior to the Christmas break.



Stockpiled material near R623 Roundabout


- The construction site will be closing on the afternoon of Friday 18th December 2020 and reopening at normal starting time on Monday 4th January 2021. We will continue to be contactable throughout this period using the contact details below.




N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

- Lane closures on the N40 eastbound will be in place between Bloomfield Interchange and Mahon Interchange and between Mahon Interchange and the Tunnel on the nights of Thursday 17th December 2020 and Friday 18th December 2020 in order to facilitate removal/adjustment of existing traffic management installations. These works will be progressed between the hours of 10 pm and 5 am on both nights and no disruption to traffic is anticipated.
- Works will continue next week on both sites on the Glanmire Road. We hope to complete at one of these sites before Xmas with works at the second site continuing up to the end of January 2021.
- We also hope to complete works on the site on the N40 eastbound before the Xmas break.



Dunkettle Live Traffic App

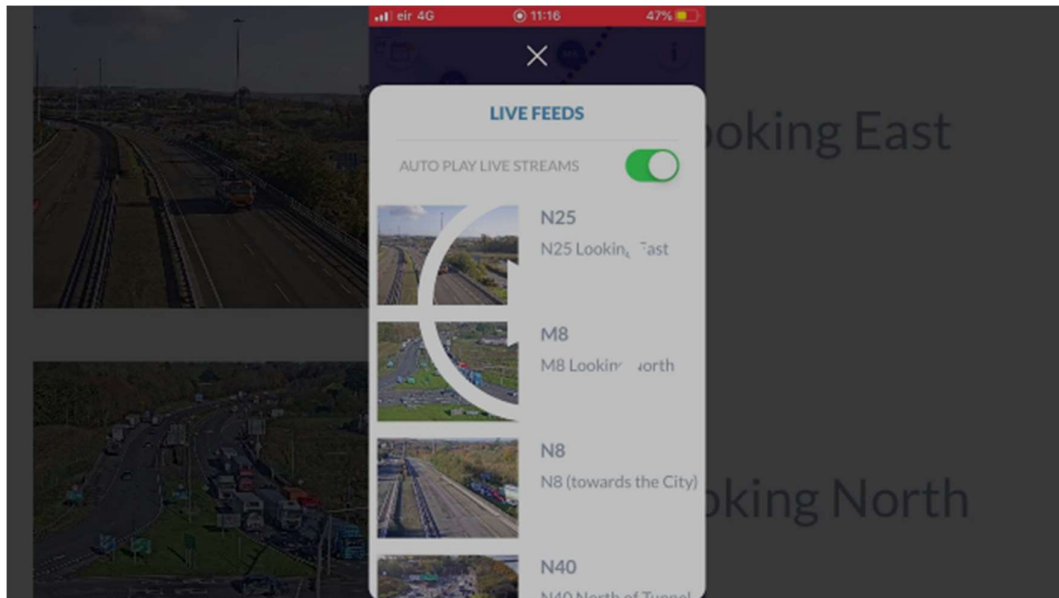

- Traffic volumes are continuing to increase significantly and this increase in traffic volume seems certain to continue over the coming fortnight. Motorists are again reminded of the availability of the Traffic App which can assist greatly in rescheduling planned journeys to avoid peak traffic times.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
