

# Dunkettle Progress Update

*22nd January 2021*

[More Information at www.Dunkettle.ie](http://www.Dunkettle.ie)



Twitter



Website

## Dunkettle Interchange Upgrade Project


*Upgrade Dunkettle to a largely free-flow interchange to alleviate traffic congestion.*

- Ground investigation works are continuing across the site and these works will now continue into February 2021.
- Works associated with the protective slab for the gas transmission main between the N25 and the Upjohn premises are nearing substantial completion. See photograph below.



**Protective slab installation works ongoing at the gas transmission main site**

- Piling works will continue in a number of areas of the site over the coming week. As part of the Interchange Upgrade works, 2 new bridge crossings of the Cork-Midleton railway line are required. These are referenced at ST08 and ST09 in the layout plan below.

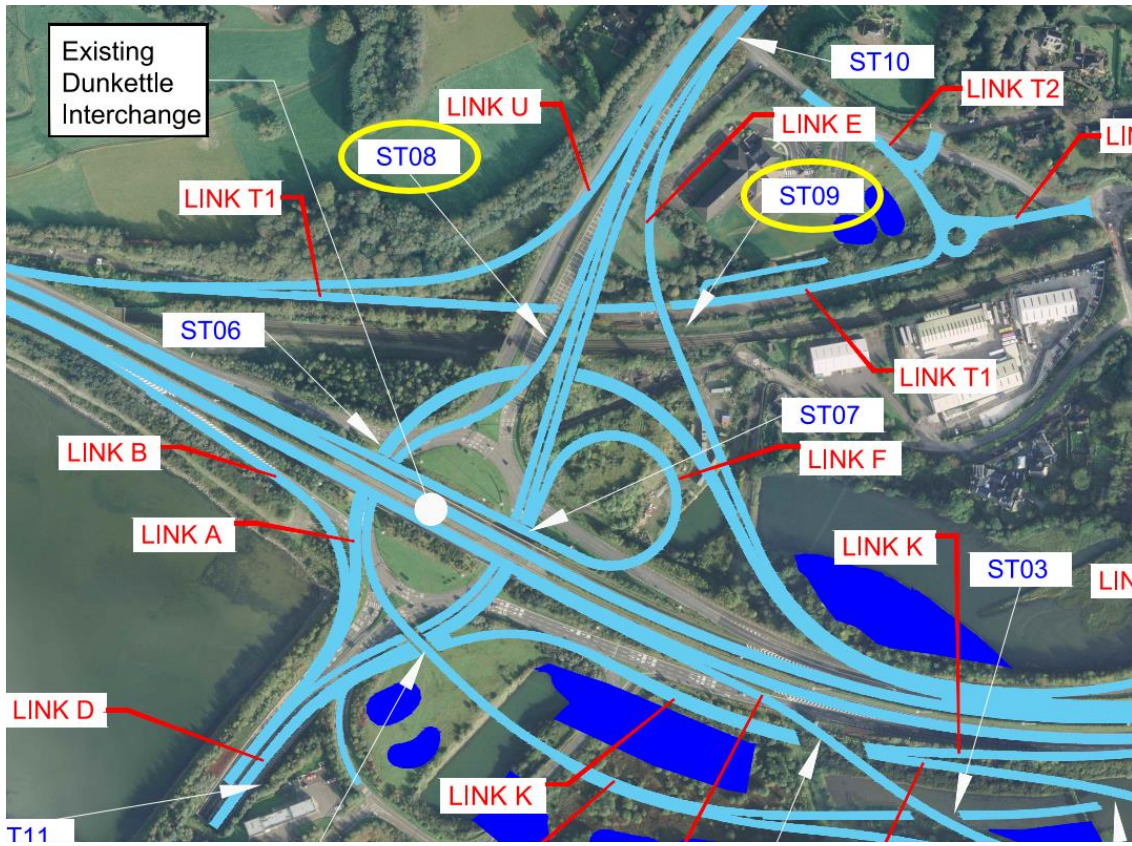

- Piling works will get underway at ST08 during week commencing Monday 25th January 2021 and enabling works under this heading are currently underway. See photograph below.



**Preparatory works for piling at new bridge structures getting underway in the area immediately east of the N8 southbound lanes. Gaelscoil Ui Drisceoil is visible in the background**

- Further site clearance works will be carried out on the N25 westbound over the coming week. The ITS traffic management measures referenced below will also be utilised to carry out these works on the Dunkettle Scheme itself.
- Excavation of the new intertidal pond will continue throughout next week. See photograph below.



**Excavation for intertidal pond continuing in the area adjoining the Project site office**

- No significant disruption to traffic is anticipated over the coming week as a result of the Interchange Upgrade works.



# N40 Intelligent Transport Systems

*Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.*

- Works associated with Intelligent Transport Systems will continue in a number of areas over the coming week, including the areas set out hereunder.
- Works at the immediate approach to Dunkettle Roundabout from the Glanmire Regional Road R639 will continue throughout next week.
- Works will get underway next week on the N8 Lower Glanmire Road outbound – the installation of service ducting at this location will necessitate closure of the slow lane. With low traffic volumes it is not anticipated that this lane closure will cause any significant disruption to traffic and works at this location will continue for a number of weeks.
- Duct installation works will continue in the verge adjoining the N25 westbound at the Little Island Interchange area. See photograph below.



- Works will continue on the M8 southbound sites for a number of weeks.
- Works will also continue on the N40 eastbound between the Mahon Interchange and the Tunnel for a number of weeks.

---

## Contact Us

As always, if there are any queries or comments in relation to these works, please contact us at:

**Phone:** 1800 810077 (at any time), **Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).



Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)

---

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).

---
