

Dunkettle Progress Update

05th November 2021

[More Information at www.Dunkettle.ie](http://www.Dunkettle.ie)




Twitter



Website

Dunkettle Interchange Upgrade Project

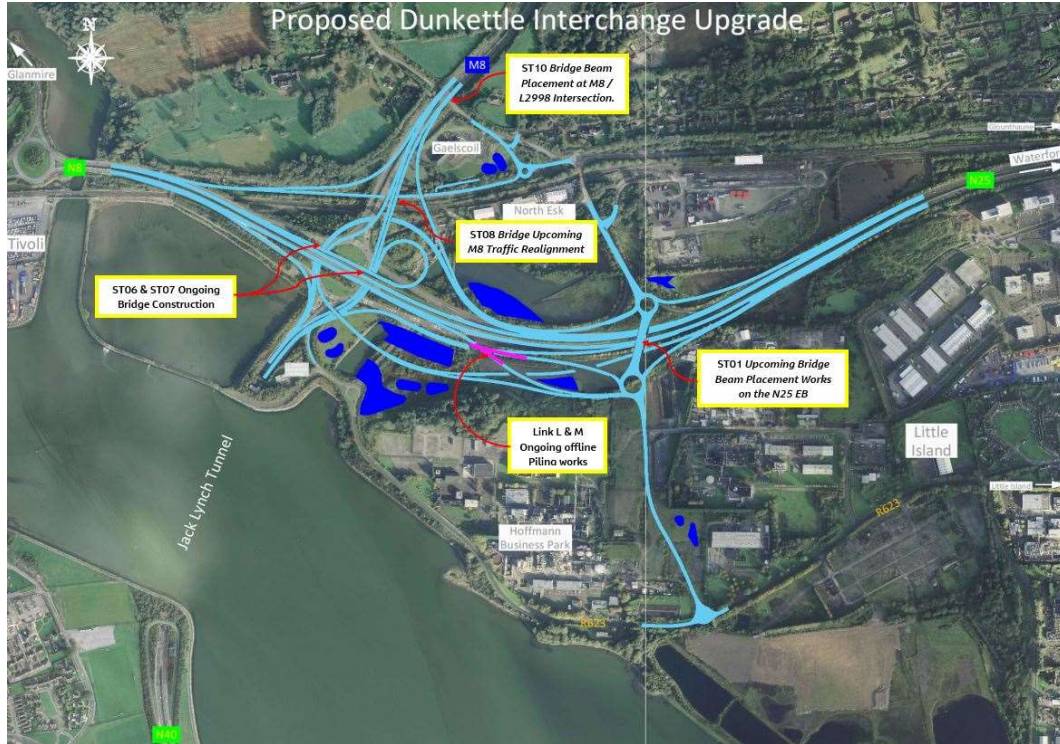

- Earthworks and works on the various new structures required for the updated alignment will continue on site over the coming period - see photograph below.



CMC Ground Improvement works ongoing for the new Link roads Link L & Link M just south of the N25 westbound.

- The beams for the central span of Structure ST01 were installed successfully last week under a closure of the N25 westbound between the Little Island Interchange and the Dunkettle Interchange Roundabout. The N25 westbound will be closed at night from 22:00 to 05:00 each night from Monday 8th to Thursday 11th November 2021 in order to facilitate the completion of the installation of GRC panels for this span of the bridge – see photograph below.



Precast concrete beams in place over the N25 westbound for Structure ST01.

- It is anticipated that the beams for the northern span of Structure ST01 over the existing N25 eastbound will be installed on Monday and Tuesday night the 15th and 16th of November 2021. In order to facilitate the works the N25 eastbound will be closed from 22:00 to 05:00 each night between the Dunkettle interchange Roundabout and the Little Island Interchange. Traffic will be diverted through Little Island via the R623.

- The precast beams will be placed at Structure ST10 tonight Friday 5th November 2021. This will require a local road closure of the L2998 from 22:00 on Friday 5th November to 05:00 on Saturday 6th November. Traffic will be diverted via the Dunkettle Roundabout and the N8/N25 to the Little Island Interchange.



Works ongoing at Structure ST10 ahead of the upcoming beam placement.

- Works will continue at Structures ST06 & ST07 at the northern side of the Dunkettle Interchange Roundabout. Further off peak lane restrictions / closures will be required in order to complete these works and details will continue to be provided to motorists as the

works are progressed – see photograph below of the ongoing works.



Construction works ongoing for Structure ST07 within the Dunkettle Interchange Roundabout.

- Over the coming period there will be a focus on finishing the new road alignment for Link D between Structure ST08 and Structure ST10 which run alongside the M8 southbound. Commuters will notice an increased level of activity in this area. Details of the upcoming Traffic Management measures will be circulated before the end of November in relation to the same – see photograph below



Waterproofing works being undertaken at Structure ST08 alongside the M8 southbound.

Dunkettle Live Traffic App

- With traffic volumes now well over 90% of pre-pandemic levels and still increasing motorists are reminded of the availability of the “Dunkettle Live” traffic app. In addition to live camera feeds, real time journey duration information is also available for all of the main routes approaches to the Dunkettle interchange Roundabout.
- This information can be extremely useful in allowing motorists to plan their journeys in periods of congestion. If you are interested in maximising the use of the ***Dunkettle Live*** App, and the

accompanying website, please click on the link hereunder for a direct link to the website.

DUNKETTLE TRAFFIC

HOME - DUNKETTLE PROJECT

LIVE FEEDS

10:26
LOCAL TIME

N25 LOOKING EAST

M8 LOOKING NORTH

N8 (TOWARDS THE CITY)

N40 NORTH OF TUNNEL

N40 - BLOOMFIELD WEST

N40 - BLOOMFIELD EAST

JOURNEY TIMES

LATEST

From	To	Travel time (minutes)
M8 J15 Glanville North	N40 J6 Kinsale Road	21 minutes
M8 J15 Glanville North	N8 Silver Springs	22 minutes
M8 J15 Glanville North	N25 J2 Little Island	8 minutes
N25 J2 Little Island	N8 Silver Springs	8 minutes
N25 J2 Little Island	N40 J6 Kinsale Road	8 minutes
N25 J2 Little Island	M8 J15 Glanville North	22 minutes
N40 J6 Kinsale Road	M8 J15 Glanville North	21 minutes

Click on the image above to see the benefits and features of the Dunkettle Traffic website; www.dunkettletraffic.ie



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

Please see hereunder link to recent drone footage showing the ongoing works at Structure 1 (ST01) on the Dunkettle Interchange Upgrade Scheme:




N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

- Works next week at the ITS sites will continue offline without any impact on traffic.
- The erection of signage on the super span gantry installed between the Bloomfield and Mahon Point Interchanges will be installed W/C 15th November 2021 to coincide with the scheduled Jack Lynch Tunnel Closures at that time – see photograph below.



Super span gantry in place spanning the N40.



As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
