

# Dunkettle Interchange Upgrade Project



More at  
[www.Dunkettle.ie](http://www.Dunkettle.ie)




## Dunkettle Progress Update *22nd April 2022*




Twitter



Website

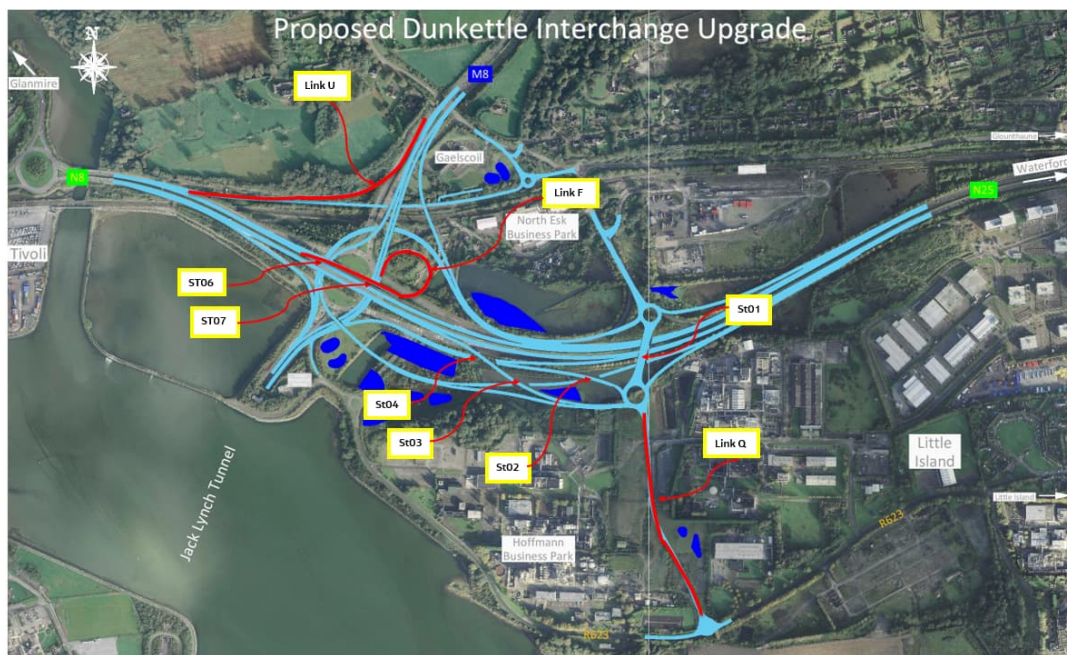

Works are continuing at the Structures St06 & St07 area, this will ultimately become free flow Link F as highlighted in red on the plan above – see photograph below also.

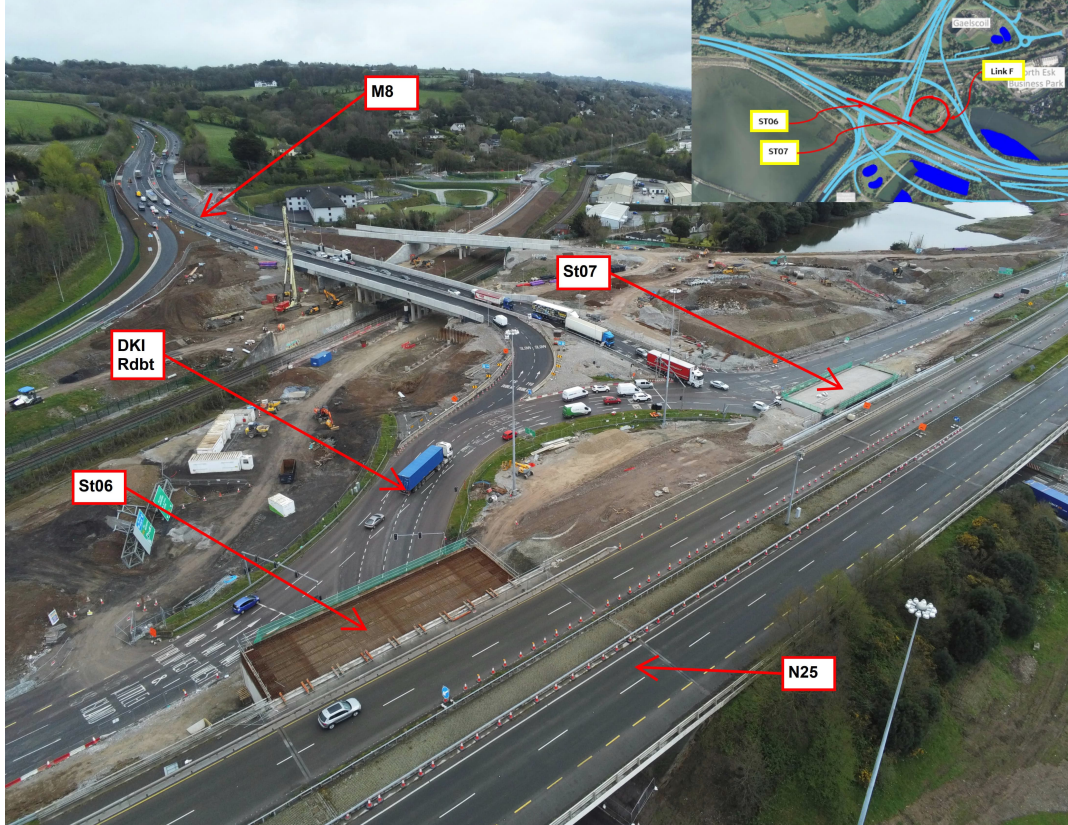


**View of Structures St06 & St07 alongside the N25 / Dunkettle Interchange Roundabout**

At Structure St01, waterproofing works are progressing and this will be followed by the surfacing of the bridge deck. We now expect that this bridge will open to construction traffic in May 2022 – see photograph below.




**Waterproofing works at St01 over the N25**

Works are progressing at Structures St02, St03 & St04 in the area south of the N25 – see photograph below.

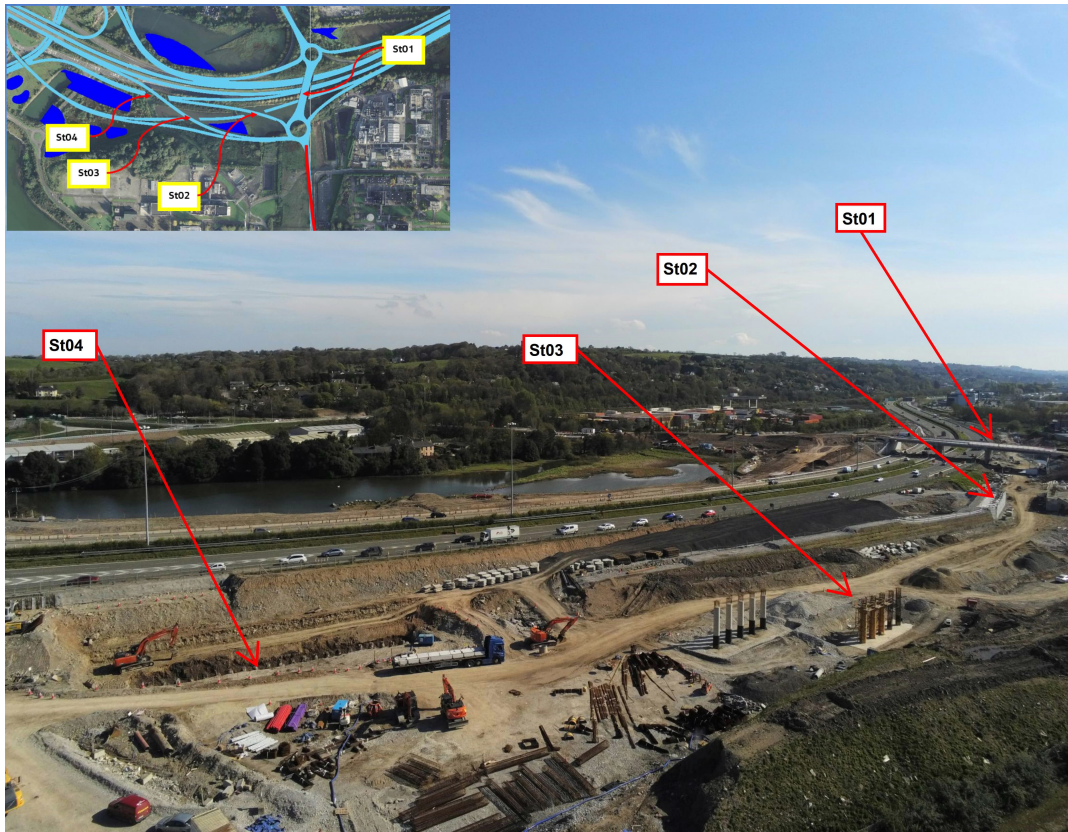

Works being progressed for St02, St03 & St04 alongside the N25 westbound

Link U, the free flow link road from the N25 eastbound to the M8 northbound (see plan below) will open to traffic this afternoon. Opening of this link road will obviously reduce traffic volumes through the Dunkettle Interchange Roundabout itself. Motorists are urged to exercise particular caution as the new road layout becomes established over the coming days.

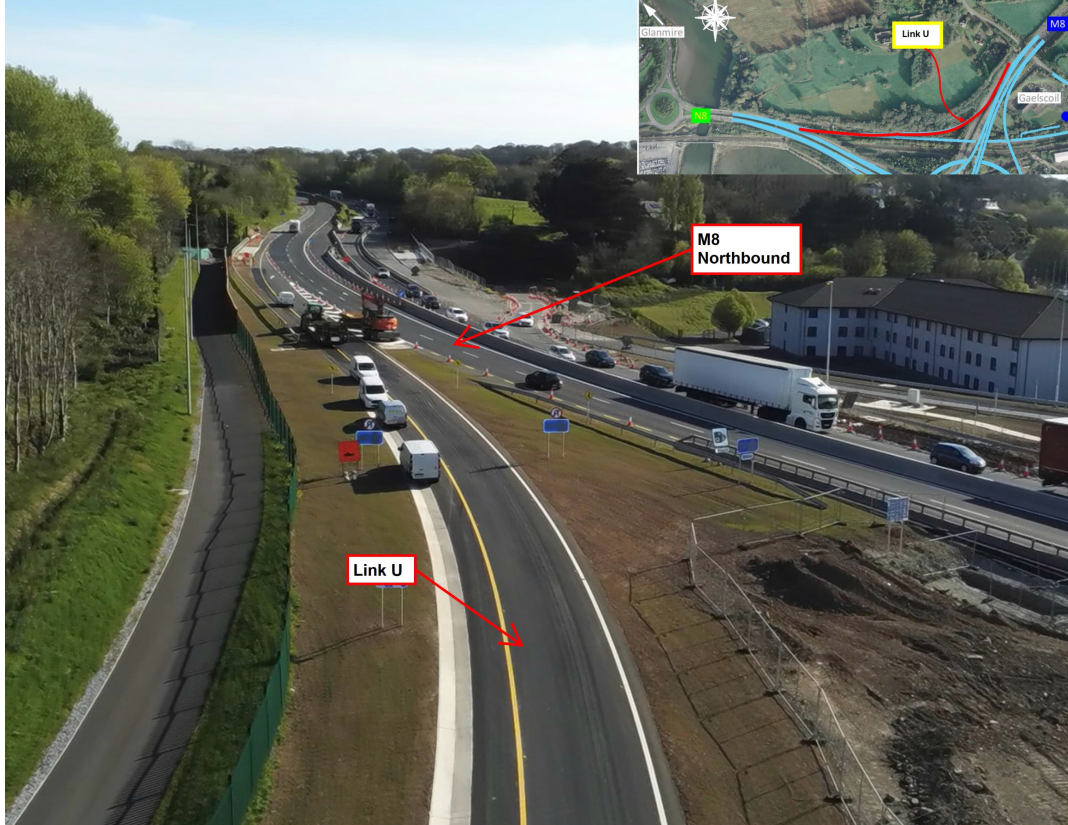

The new Link U merge from the N25 eastbound with the M8 northbound

The link below, to this weeks video, should also provide motorists with a useful indication of the Link U layout.

In overall terms the works remain on track for completion by the due date of February 2024.

We have received a number of queries in relation to closures of the southbound bore of the Jack Lynch Tunnel over recent weeks. We understand that the Tunnel Management Contractor is carrying out the appropriate investigative works with the electronic over height vehicle detection system and we further understand that any issues arising will be addressed over the coming days.

**Link U Layout - The new free flow link from the N25 eastbound to the M8 northbound**



## Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.





**Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)**

# N40 Intelligent Transport Systems

*Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.*

Works next week will continue to focus on the commissioning of the new ITS equipment on the N40 northbound approach to the tunnel during the scheduled tunnel maintenance closures.

As always, if there are any queries or comments in relation to these works, please contact us at:

**Phone:** 1800 810077 (at any time),

**Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).

Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



**More at**  
**[www.Dunkettle.ie](http://www.Dunkettle.ie)**



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).

This email was sent to <<Email address>>

[why did I get this?](#) [unsubscribe from this list](#) [update subscription preferences](#)

N40/Dunkettle Team · Tunnel Management Building · Dunkettle · Glanmire, CO. CORK T45 E898 · Ireland
