

Dunkettle Progress Update


06th May 2022



Twitter



Website

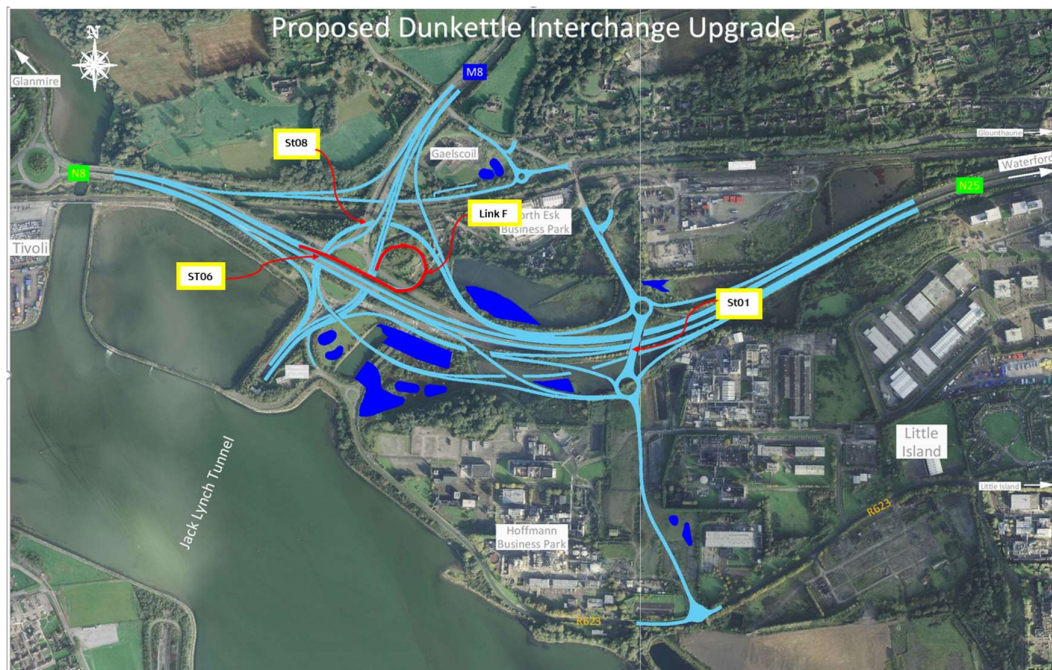

- At Structure St01, works on the bridge deck have been completed, including the initial surfacing layer.

- Also in the area of Structure St01, earthworks north and south of the structure are progressing well – see photograph below.



Embankment construction ongoing north of Structure St01.

- Structure St01 is now open to construction traffic only, this will allow us to transfer material between the sections of the project both north and south of the N25 without interfering with traffic in the area.



Construction traffic utilising Structure St01 to cross over the N25.


- As noted in last week's update, construction of the columns at Structure St08 is now underway – see photograph below. We now expect that the first columns in this area will be cast week commencing 09/05/22.



Works being progressed at Structure St08 ahead of the upcoming column construction works.

- At Structure St06 (i.e. the structure on the new free flow Link F from the Glanmire Roundabout to the Jack Lynch Tunnel), preparatory

works associated with the bridge deck are nearing completion with the deck due to be poured at night on Thursday 12th May 2022 – see photograph below.

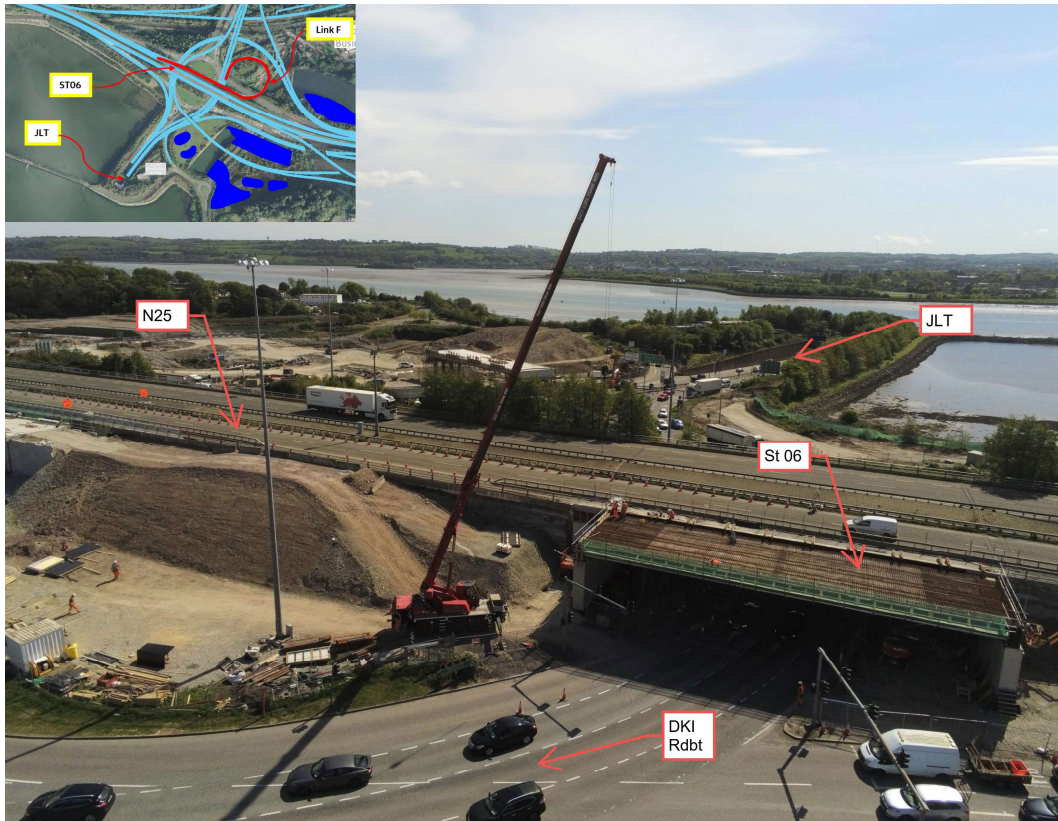


Works being progressed at Structure St06 for the upcoming bridge deck pour.

This week's progress update shows the route of the proposed new link road, Link C. Upon completion, this will be the new free flow link from the N25 westbound to the M8 northbound



Dunkettle Live Traffic App

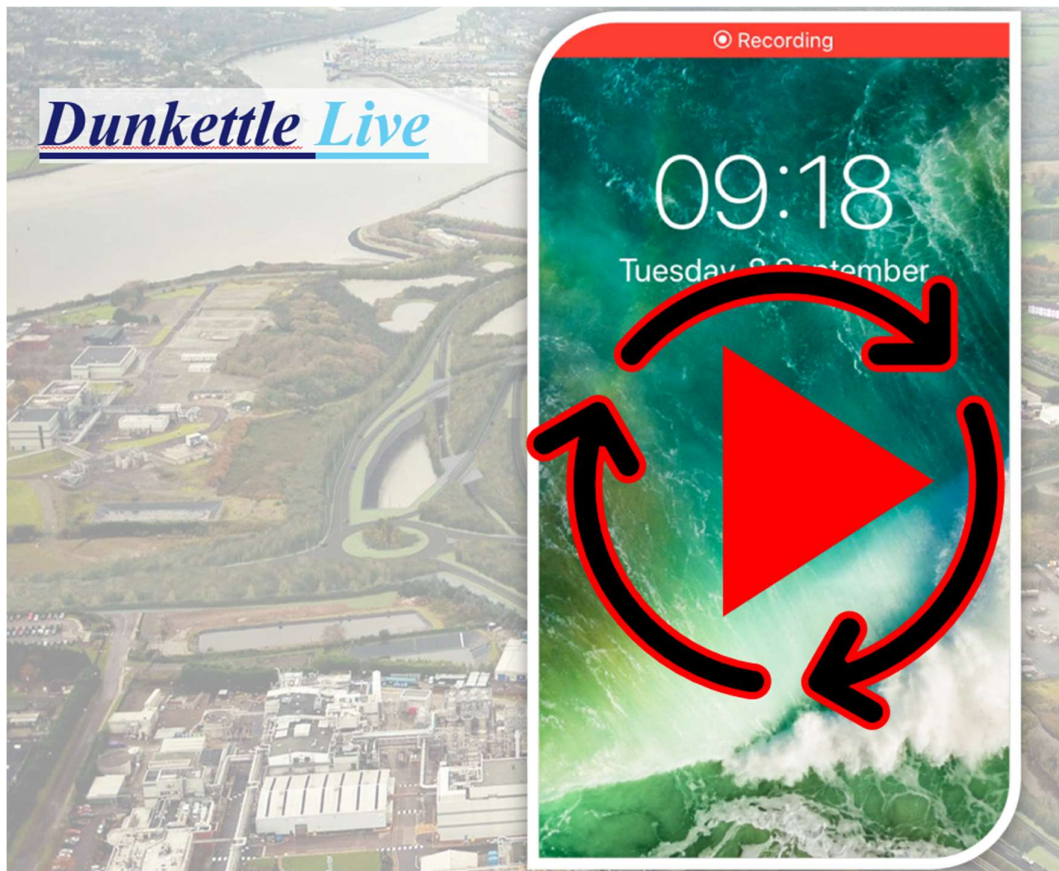

Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

- Works next week will continue to focus on the commissioning of the new ITS equipment on the N40 northbound approach to the tunnel with no impact on traffic

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.

Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the
N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
