

Dunkettle Progress Update


13th January 2023



Twitter




Website

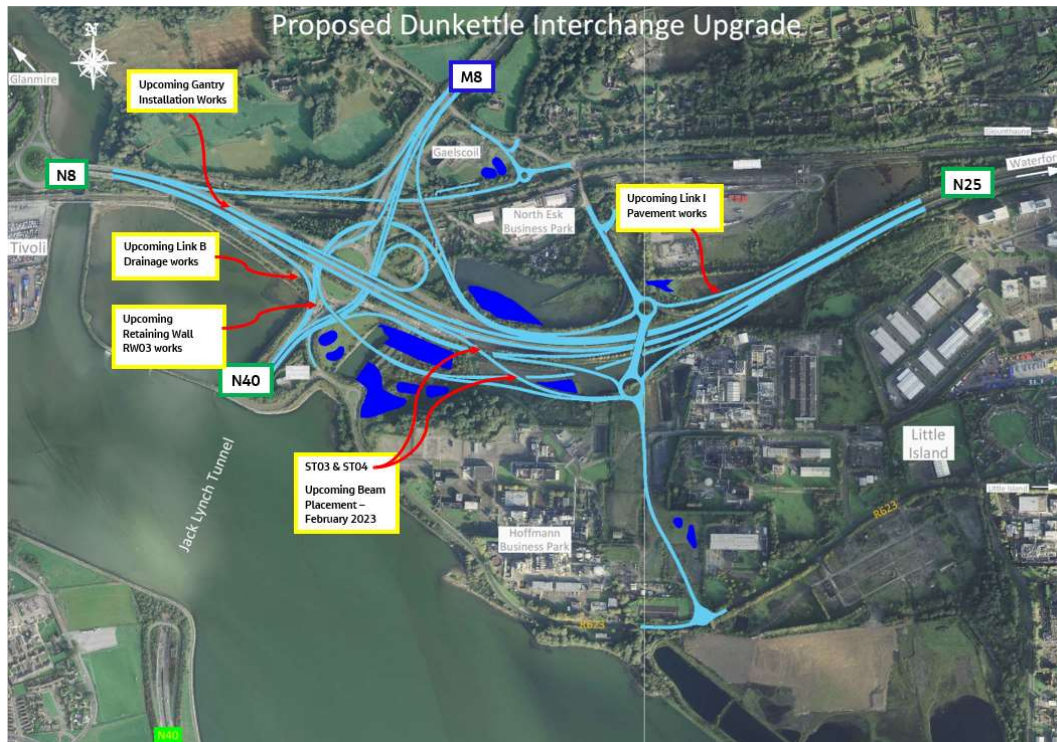


- Motorists are again reminded that speed control measures, coupled with CCTV monitoring are in place across the site and will remain in place over the coming months.

- Localised lane restrictions will be in place on the right hand side of the N40 northbound approach to the Dunkettle Interchange Roundabout during off peak times on Monday, Tuesday and Wednesday of next week from 09:30 to 15:30. Thereafter, the lane restriction will be in place continuously from 19:00 on Wednesday 18th January 2023 with the lane fully reopened by 17:00 on Saturday 21st January 2023. The lane restriction will be limited to the short N40 northbound lane at the immediate approach to the roundabout traffic lights heading towards the M8 northbound – see photograph below. No significant disruption is anticipated as a result of the same at off peak times, but slight delays may be experienced by N40 northbound traffic on Thursday 19th and Friday 20th January 2023. Traffic flow will be monitored continuously to ensure that any impact which does occur is minimised. This is required in order progress the new Retaining Wall RW03 in this area.

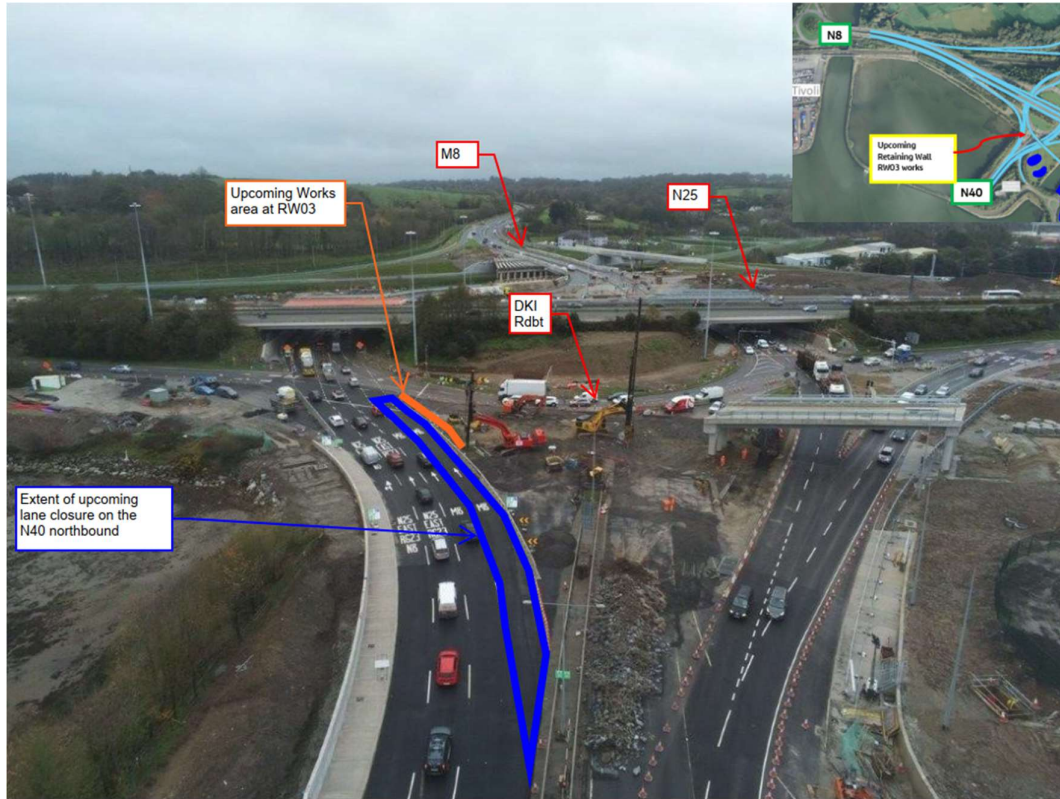


Upcoming works area and lane closure extent at RW03 alongside the N40 northbound.

- Surfacing works will recommence on site from Monday 16th January 2023. We hope to complete the surfacing works at Link I during W/C 16th January 2023. The focus for the surfacing works will then switch back to the central median of the N25 – see photograph below.

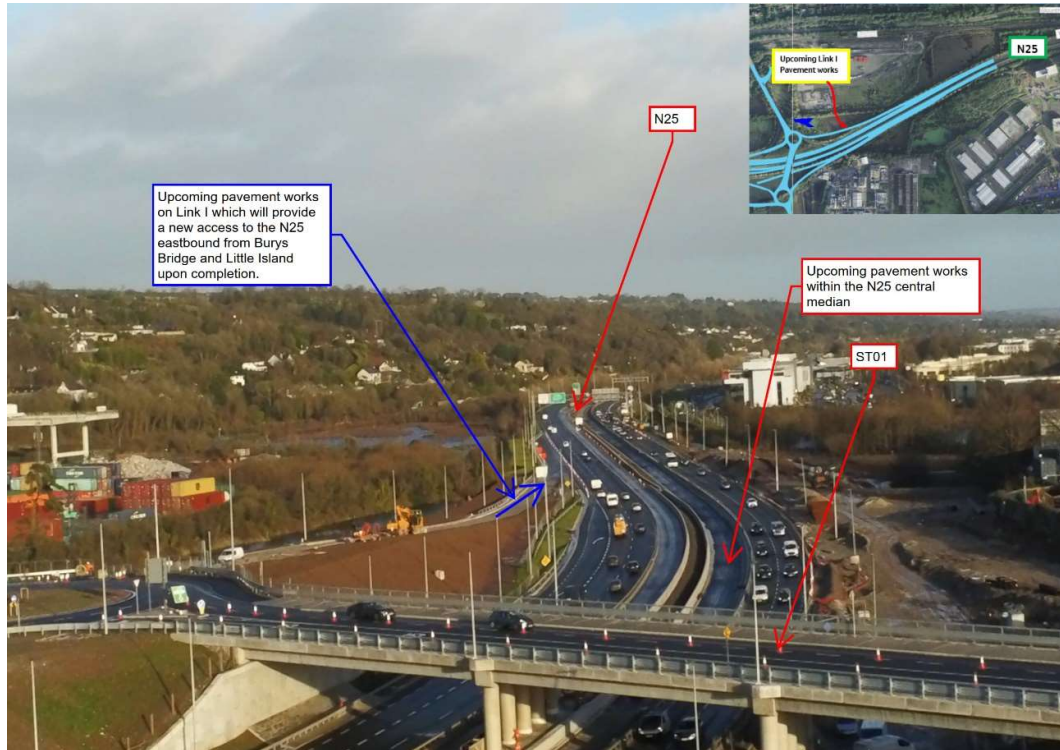


Preparatory works ongoing on Link I alongside the N25 eastbound in advance of the upcoming pavement works.

- From a Structures point of view, the focus over the coming period will be on the completion of Structures ST03 & ST04. We hope to place the beams at both of these structures by the end of February 2023 – see photograph below.

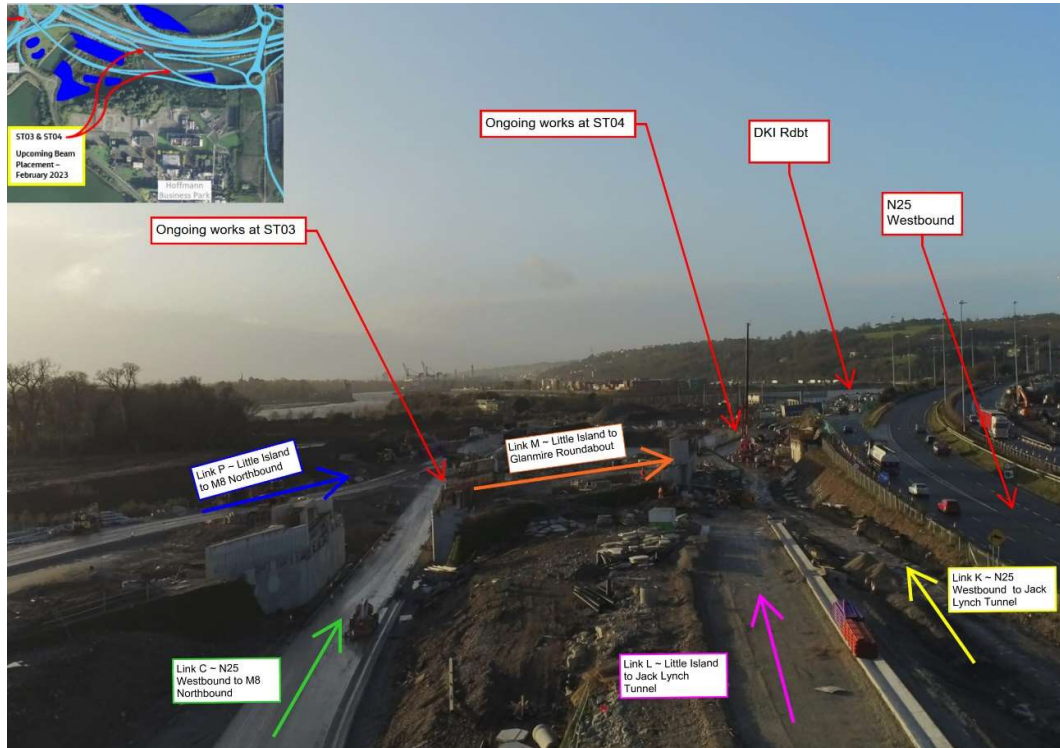

Works ongoing at Structures ST03 & ST04 alongside the N25 westbound.

- Drainage and general roadworks will recommence at Link B this month. We hope to complete this work and open Link B by the end of February 2023 also – see photograph below.

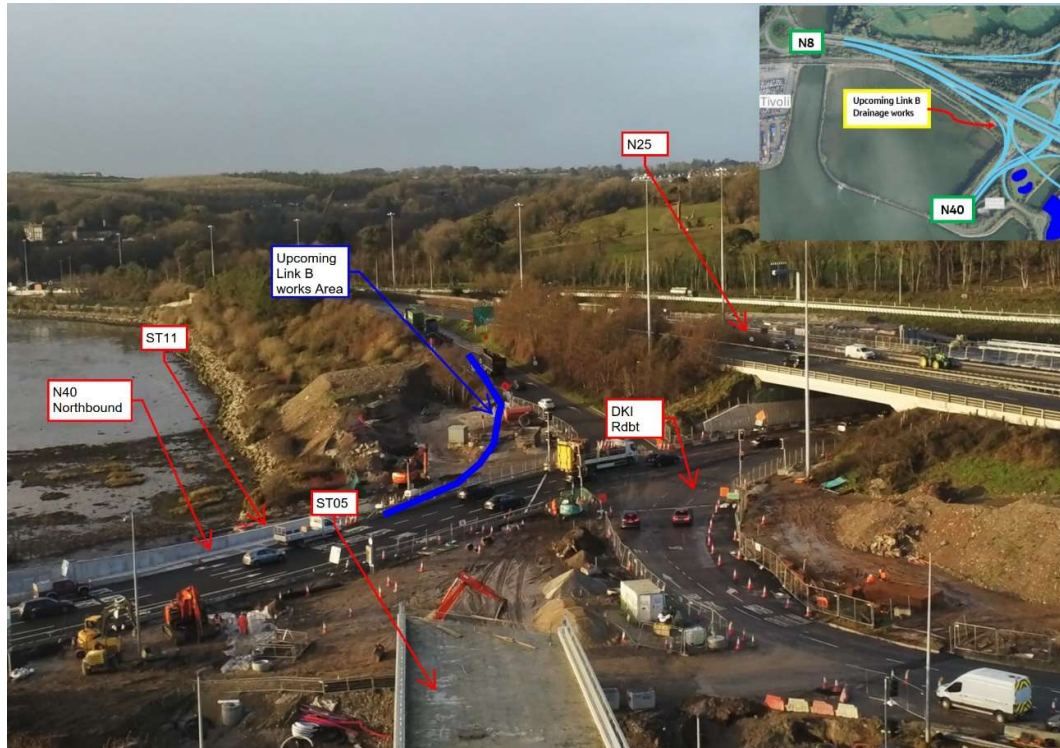

Upcoming works area at Link B alongside the merge towards the N8 westbound from the DKI Rdbt.


- A number of permanent signage gantries will also be installed at various locations over the coming period under night-time working – see photograph below.



Gantry signage installation works ongoing on the N25 under night-time working.

- In overall terms, the works remain on track for completion by the due date of February 2024.

Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
