

# Dunkettle Progress Update


## *03rd February 2023*



Twitter




Website

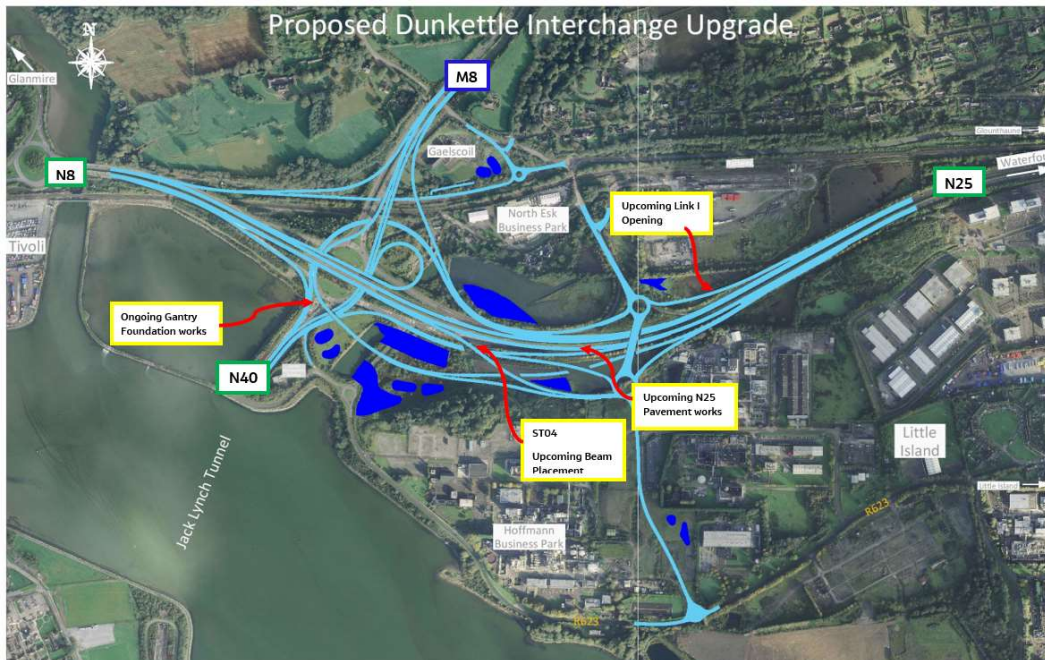


- Motorists are again reminded that speed control measures, coupled with CCTV monitoring are in place across the site and will remain in place over the coming months.

- Unfortunately, the opening of Link I has been delayed slightly to allow time for the completion of the pedestrian / cyclist traffic light-controlled crossing point. We now expect that this link will open to traffic during W/C Tuesday 7th February 2022 – see photographs below.

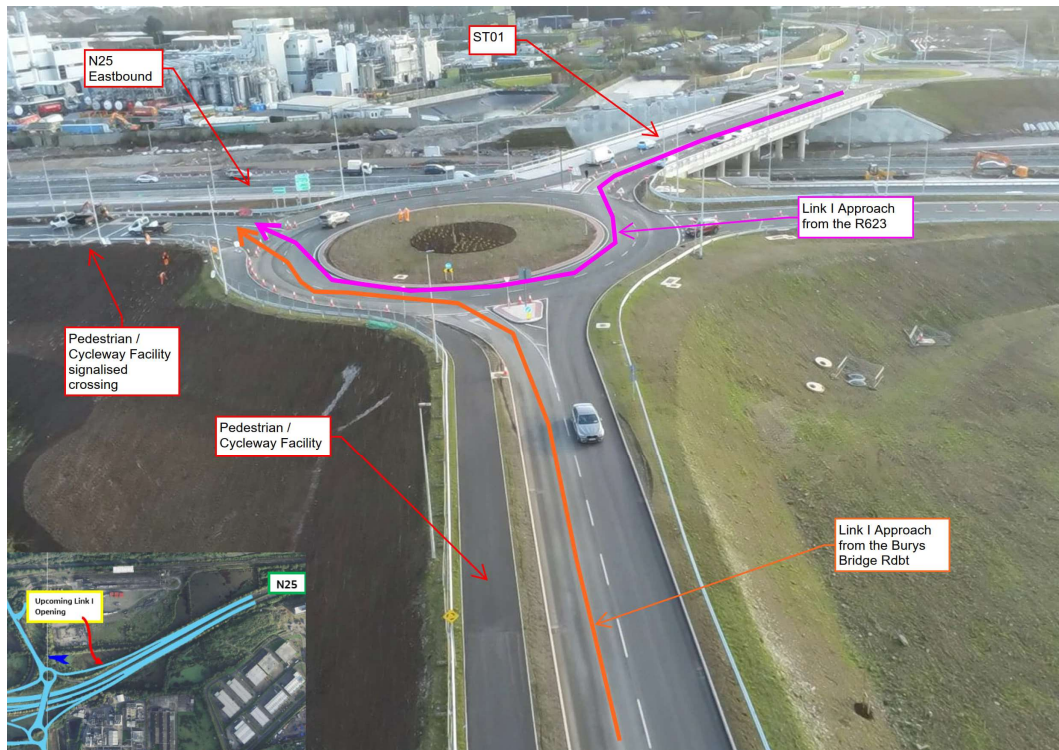


The approach to Link I from the R623 Roundabout and the Bury's Bridge Roundabout.

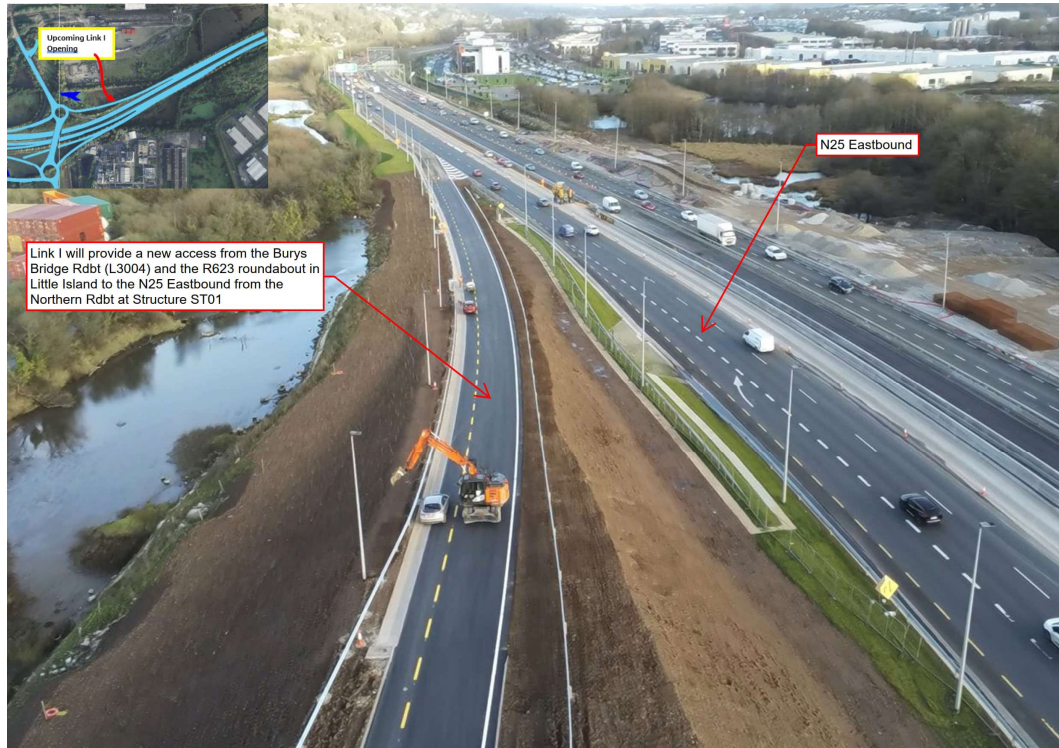

**Finishing works being completed in advance of the opening of Link I.**

- We now propose to construct the gantry base for the proposed portal directional signage at the southern side of the interchange roundabout circulating carriageway over the coming days. Accordingly, while the Retaining Wall RW03 works have reached completion at this location for the time being, the localised lane restriction on the N40 northbound immediate approach to the interchange roundabout will remain in place for another week or so approximately – see photograph below. No significant disruption to traffic is anticipated as a result of the same.



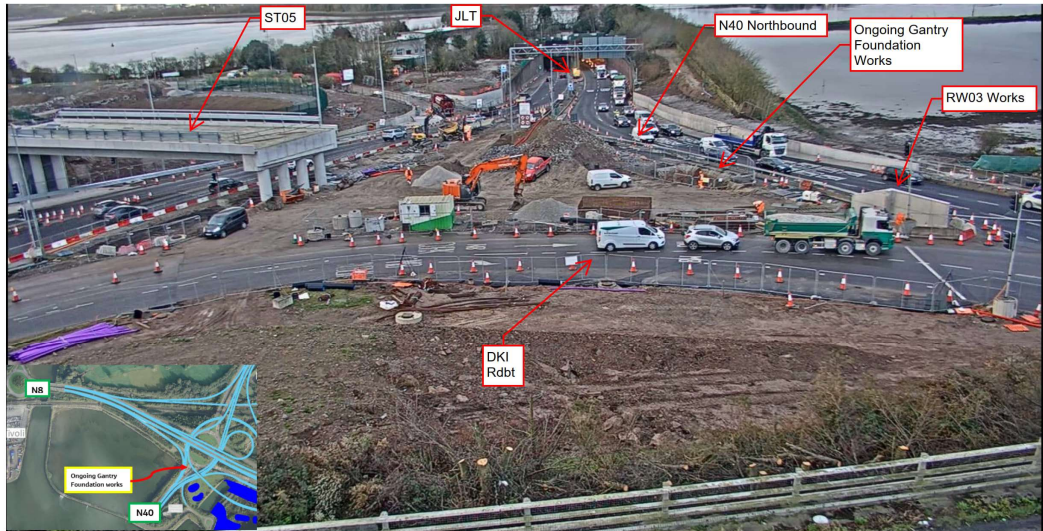

**Works ongoing for the new gantry foundation alongside the N40 northbound.**

- We now intend to place the bridge beams at Structure ST04 during daytime working hours on Wednesday 8th and Thursday 9th February 2023 with a 5am start each morning. These works are offline and should cause no disruption to traffic but they will be very visible to motorists on the N25 westbound in particular - see photograph below.



**Structure ST04 alongside the N25 Westbound ready for the installation of beams.**


- Surfacing works will be focused on the N25 median area and the N25 westbound for a number of weeks starting from Tuesday 7th February 2023 – see below photograph of the ongoing preparatory work for the same.



Preparatory works being completed within the N25 central median in advance of the upcoming pavement works.



**This week's video shows the route of Link I which will provide a new access for commuters from the R623 Roundabout and the Burys Bridge Roundabout to the N25 Eastbound.**



# Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)



---

As always, if there are any queries or comments in relation to these works, please contact us at:

**Phone:** 1800 810077 (at any time), **Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).



Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



---

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).

---
