# Dunkettle Progress Update 13th November 2020

#### More Information at www.Dunkettle.ie





#### **N40 Intelligent Transport Systems**

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

 Structural steelworks required to support the ITS equipment itself is currently being progressed at five ITS sites on approach to Dunkettle Interchange. See photograph below.



Support steel being installed under night time working on the N40 eastbound in the area of Bloomfield Interchange

- The steelwork has been installed at both eastbound sites on the N40, on the southbound site on the M8, and on the eastbound site on the N8 at Tivoli. The steelwork at the remaining site on the N40 westbound will be progressed under night time working on tonight Friday 13<sup>th</sup> November 2020 starting at 10.00 pm. Traffic management associated with tonight's work will be removed before 6.00 am on tomorrow morning, 14<sup>th</sup> November 2020.
- Works will get underway on remaining ITS sites on the various approaches to Dunkettle Interchange before Christmas and details under this heading will follow in future updates.

## Dunkettle Interchange Upgrade Project

Upgrade Dunkettle to a largely free-flow interchange to alleviate traffic congestion.

 Construction works are continuing in the area between the N25 westbound and the Upjohn premises in association with installation of protective slab to the gas transmission main at this location. See photograph below.



Reinforcement steel in place in preparation for concrete pour at the gas transmission main site


• The new footway/cycleway leading east from the Dunkettle Roundabout will open on next Monday 16<sup>th</sup> November 2020. See photograph below.



View of the new footway/cycleway facing east from the Glashaboy River

 To date approximately 20,000 tonnes of material have been stockpiled on the proposed new link road immediately west of the Upjohn premises. This stockpiling operation will continue into the New Year with the material import works causing no disruption to traffic.

### **Dunkettle Live Traffic App**

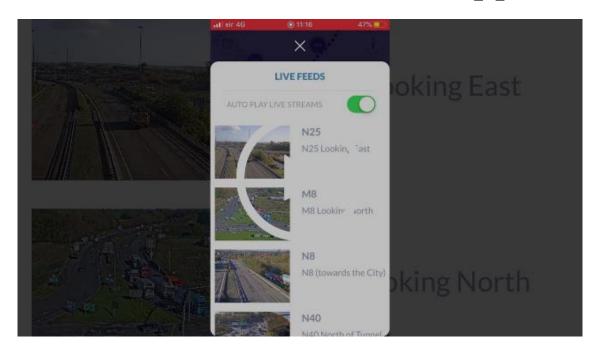

 With traffic volumes likely to increase significantly over the coming weeks, motorists are again reminded of the availability of the Traffic App. The App will assist greatly in rescheduling planned journeys to off-peak times.









Dunkettle Live App: Download from Apple App store or from Google Play store

As always, if there are any queries or comments in relation to these works, please contact us at: **Phone:** 1800 810077 (at any

time), Email: roadconstruction@ccc-site.com.

Acomhal Dhún Citil Dunkettle Interchange

Further information on the Dunkettle Scheme can be accessed <a href="https://www.dunkettle.ie">www.dunkettle.ie</a>.

Real time traffic information can be accessed via <a href="www.dunkettletraffic.ie">www.dunkettletraffic.ie</a> or on the Dunkettle Live App (<a href="Apple App store">Apple App store</a> and <a href="Google Play store">Google Play store</a>). New subscribers to the newsletter can

register: www.dunkettle.ie/newslettersignup
