

Dunkettle Progress Update


27th May 2022



[Twitter](#)




[Website](#)

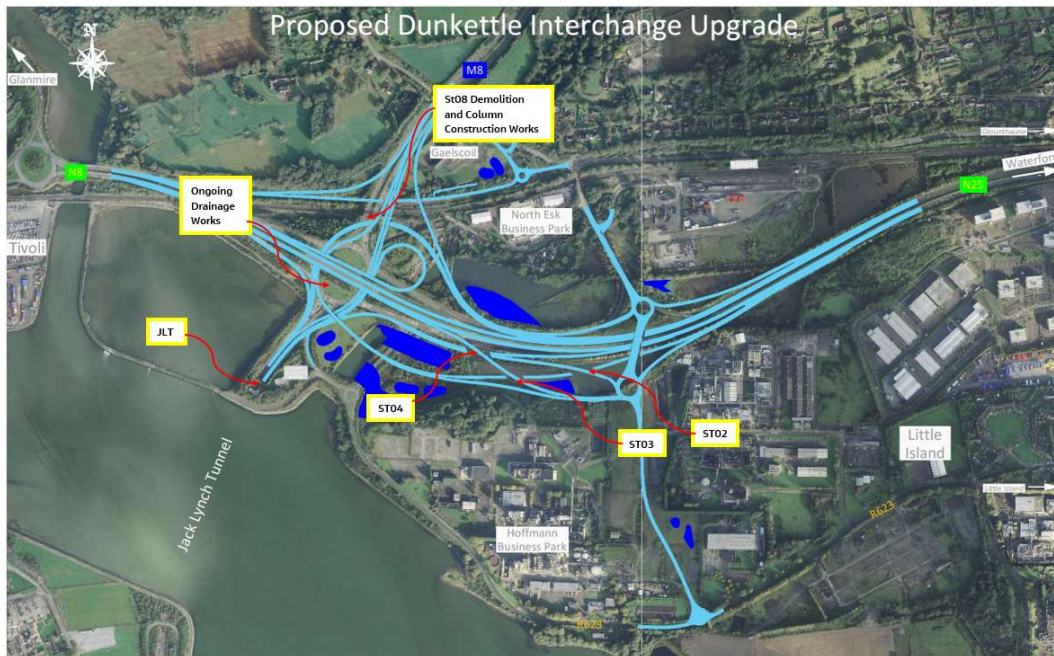

- Works are continuing across the site at all structures and embankment construction areas. Works are still largely offline, but a number of online works items will get underway over the summer months. As always, details of these works will be issued in advance via the weekly newsletter.

- Works are ongoing in the southern half of the Interchange Roundabout centre island. New drainage lines are being installed to ensure that the overall interchange area will be drained appropriately upon completion of the project – see photograph below.

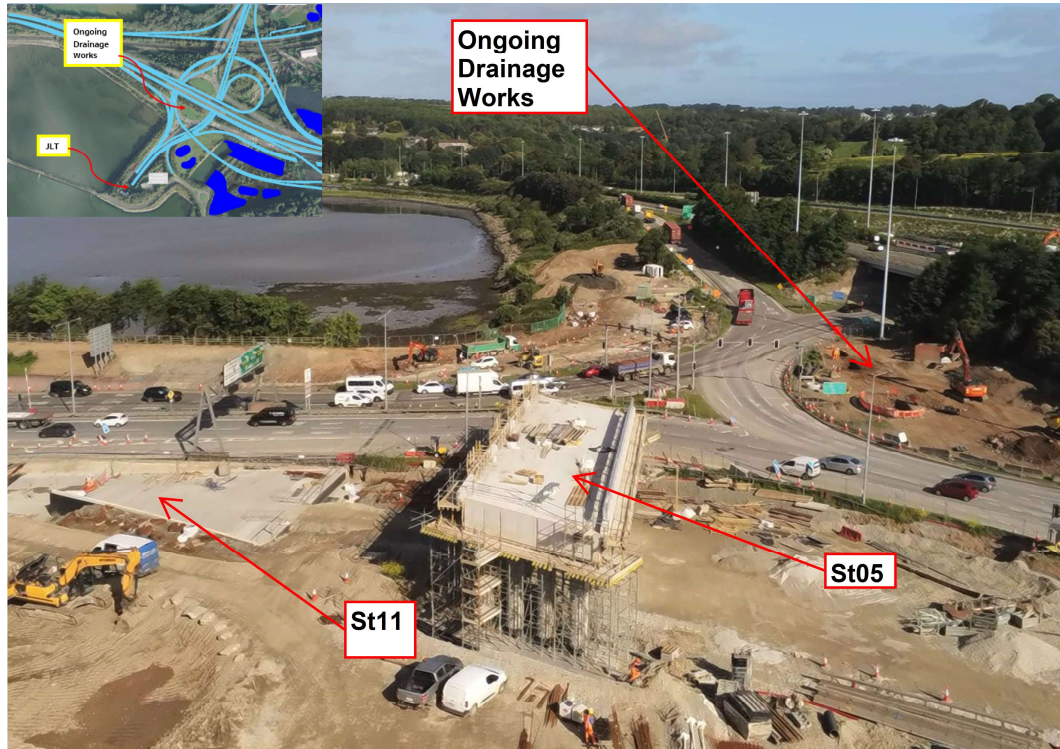

Drainage works being completed at the with the centre island of the Interchange Roundabout.

- Works on Structures St02, St03 & St04 are continuing at the southern side of the N25 westbound. At the southern abutment of Structure St04, column construction work is progressing. Structure St04 will probably be one of the last structures to be completed due to the interface of the northern section of Structure St04 with the N25 westbound– see photograph below.



Works ongoing for Structure St04 alongside the N25 westbound.

- Demolition works at the existing railway bridge are heading towards completion at the location of Structure St08 – see photograph below. We expect that these works will be completed in June 2022. Column construction works associated with the new Structure St08 are continuing at this location.




Demolition works ongoing at the old M8 railway bridge.

This week's progress update shows ongoing works in the vicinity of the Dunkettle Interchange Roundabout



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

N40 Intelligent Transport Systems

Installation of gantry mounted Variable Message Signs and other infrastructure to display traffic information such as journey times.

- Works continued to focus on the commissioning of the new ITS equipment this week on the N40 northbound approach to the tunnel

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.

Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the
N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
