

Dunkettle Progress Update


05th August 2022



Twitter



Website

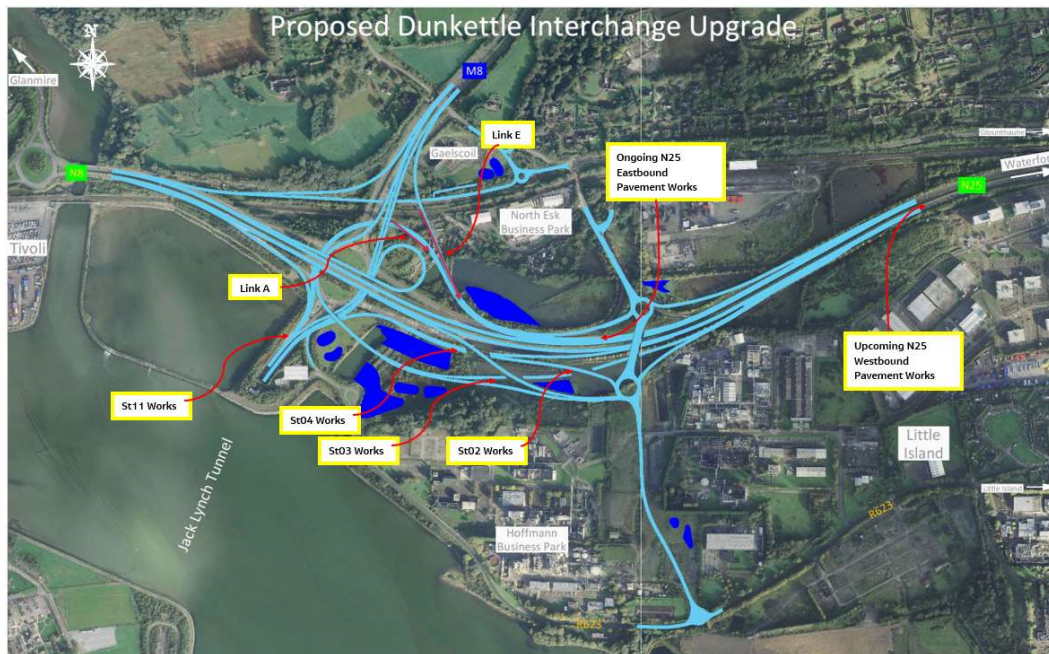


- Motorists are again advised in relation to the speed control measures which will be in place regularly on the Dunkettle Interchange site over the coming weeks.

- Works at Structures St02, St03 & St04 are continuing offline alongside the N25 westbound. The next major element of construction will be the placement of the bridge beams at Structure St02 which we expect to take place next week (W/C 08/08/2022) – see photograph below




Works ongoing at Structures St02, St03 & St04.

- Structure St11 is the new retaining wall on the N40 southbound approach to the Jack Lynch Tunnel and works are progressing well here with a further foundation poured this week at the eastern side of the Structure – see photograph below.

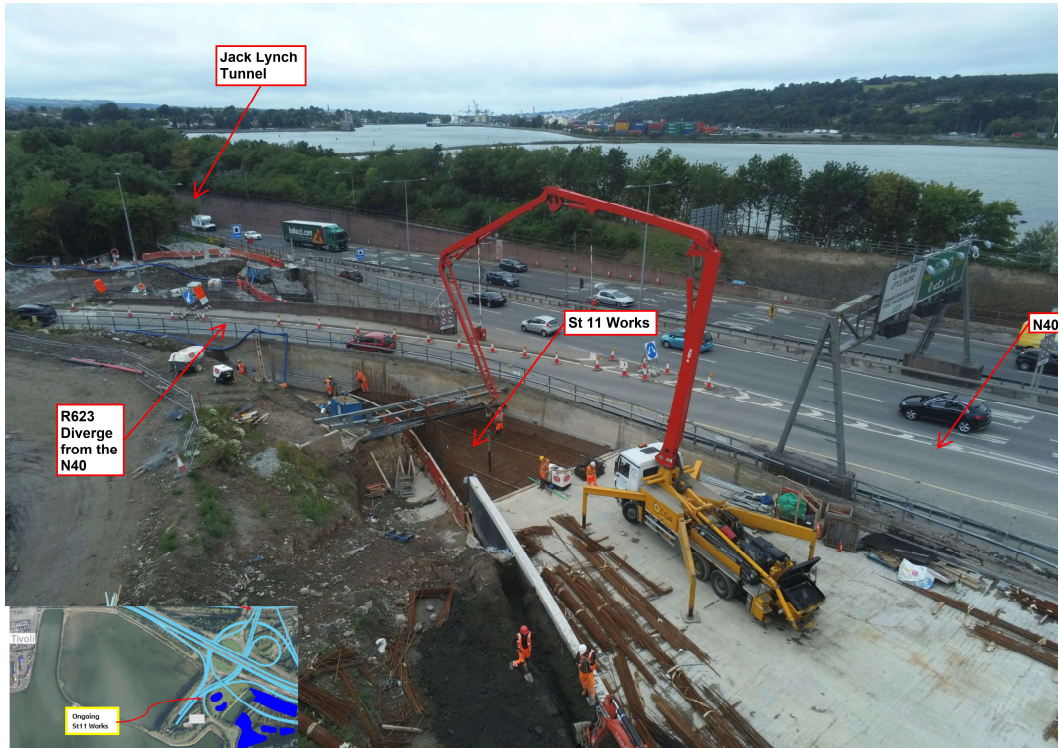


Works ongoing at Structure St11.

- Surfacing works will now recommence on the N25 eastbound early next week (W/C 08/08/2022). These eastbound site works will generally be progressed under night time working – see photograph below.

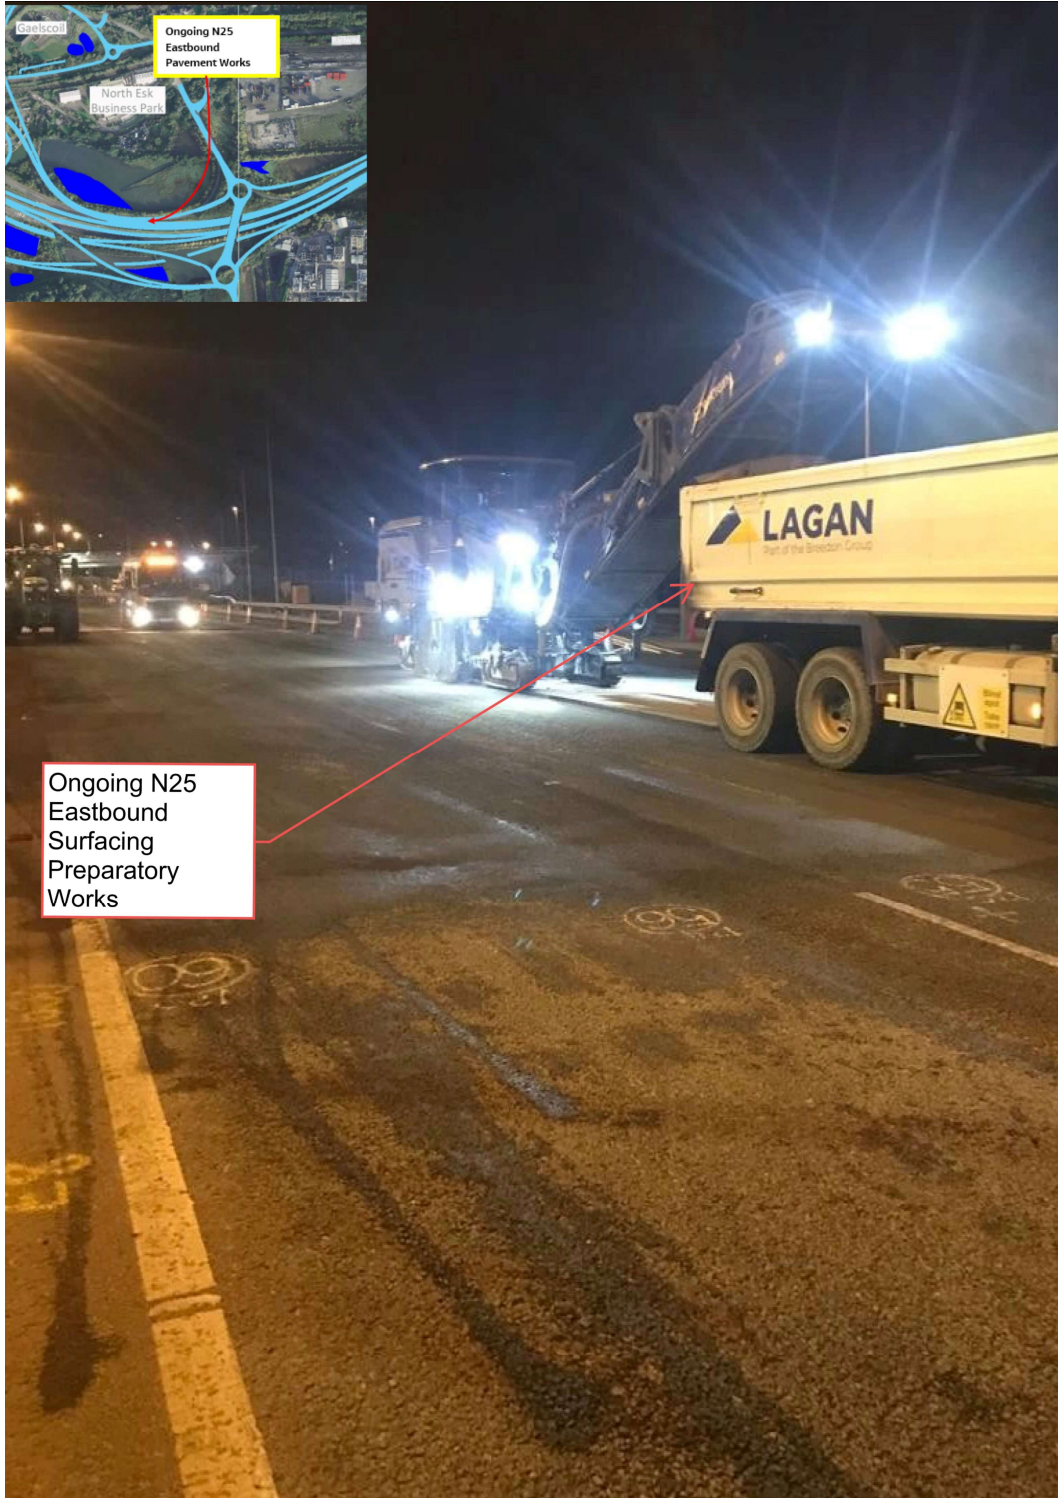

Preparatory works ongoing on the N25 eastbound.

- Surfacing works over the last week have focused in the offline areas of Link A & Link E which will merge with the N25 eastbound – see photograph below.

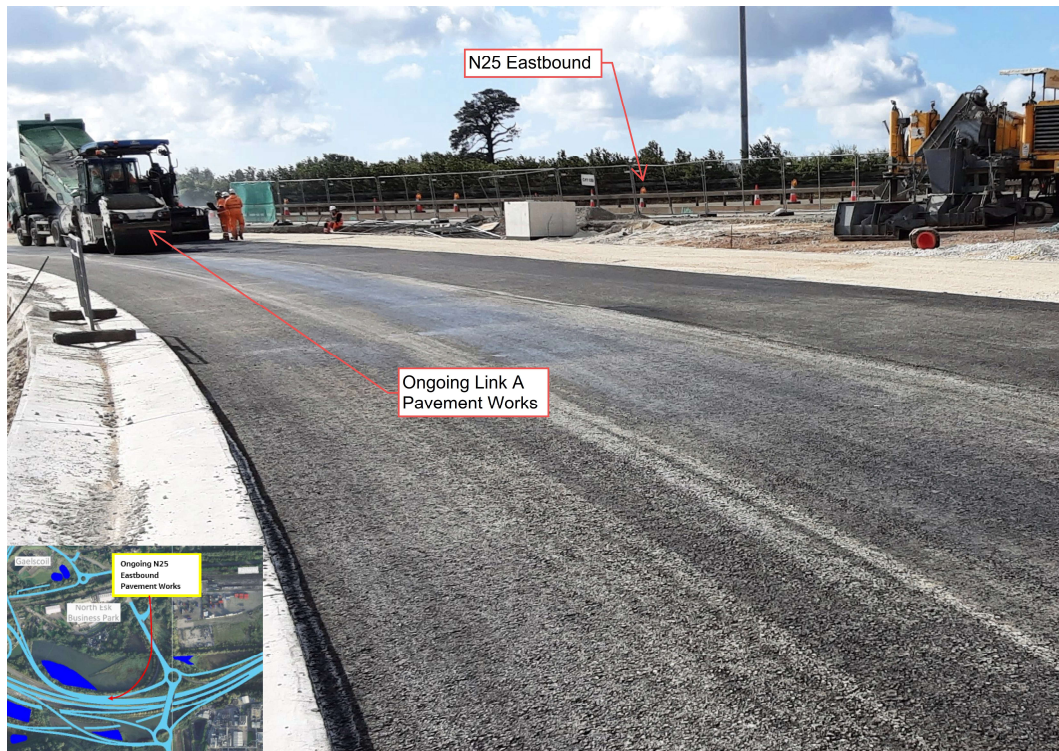


Pavement works being progressed offline in the Link A & E areas.

- On the westbound side of the N25, significant weekend traffic restrictions will be required to facilitate the upcoming surfacing works starting (subject to suitable weather conditions) on the weekend of Friday 19th August 2022. Full details of the restrictions will be provided in next week's update.

**This weeks video shows the ongoing works in the vicinity of Link C
at the southern side of the N25**



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)



As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.

Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
