

# Dunkettle Progress Update


## *06th April 2023*



[Twitter](#)



[Website](#)

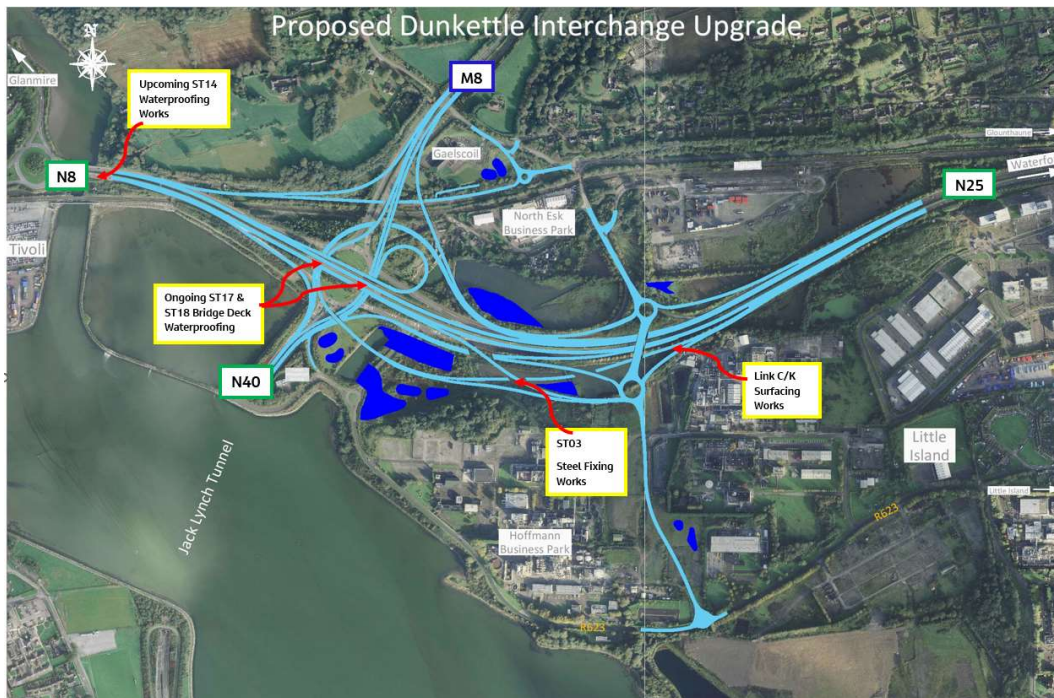


- Motorists are again reminded that speed control measures, coupled with CCTV monitoring are in place across the site and will remain in place over the coming months.

- From a Structures point of view, steel fixing works at Structure ST03 are progressing well and we hope to pour the bridge deck of this Structure during week ending Friday 14th April 2023 – see photograph below.




**Steel Fixing Works ongoing at Structure ST03.**

- Surfacing works are currently focused on what will ultimately become Link K in the area of Structure ST01 - see photograph below. These works will continue over the coming period.

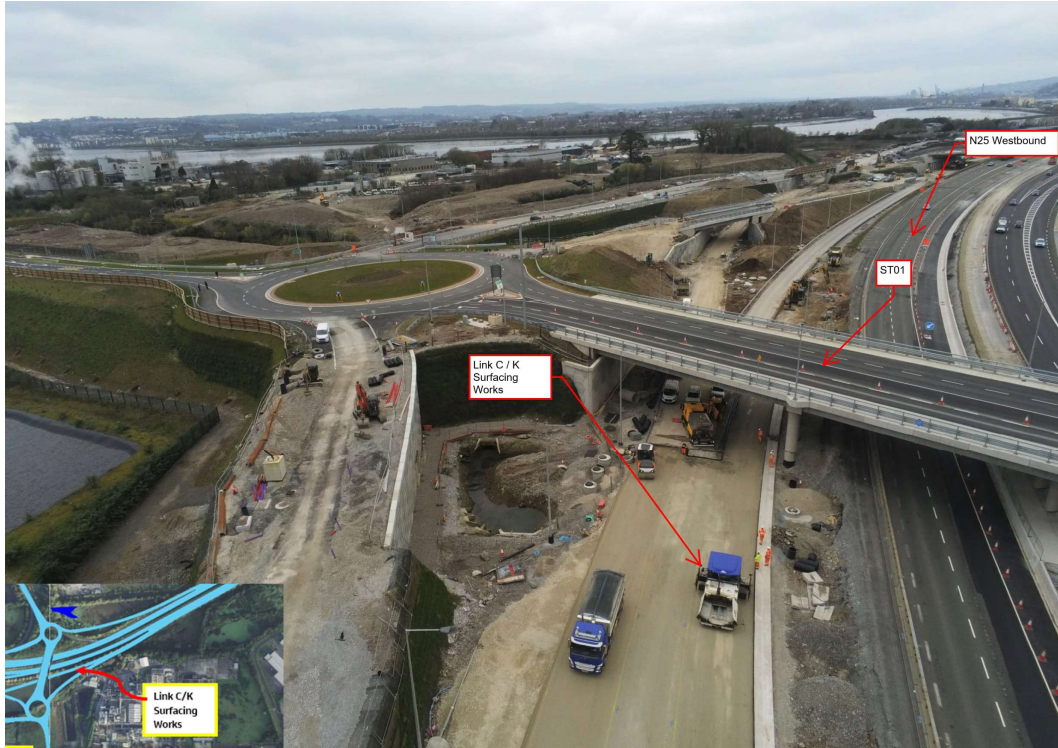

Surfacing works ongoing for Link K alongside the N25 westbound.

- At the Interchange bridges, renewal of the bridge deck waterproofing is continuing – see photographs below.

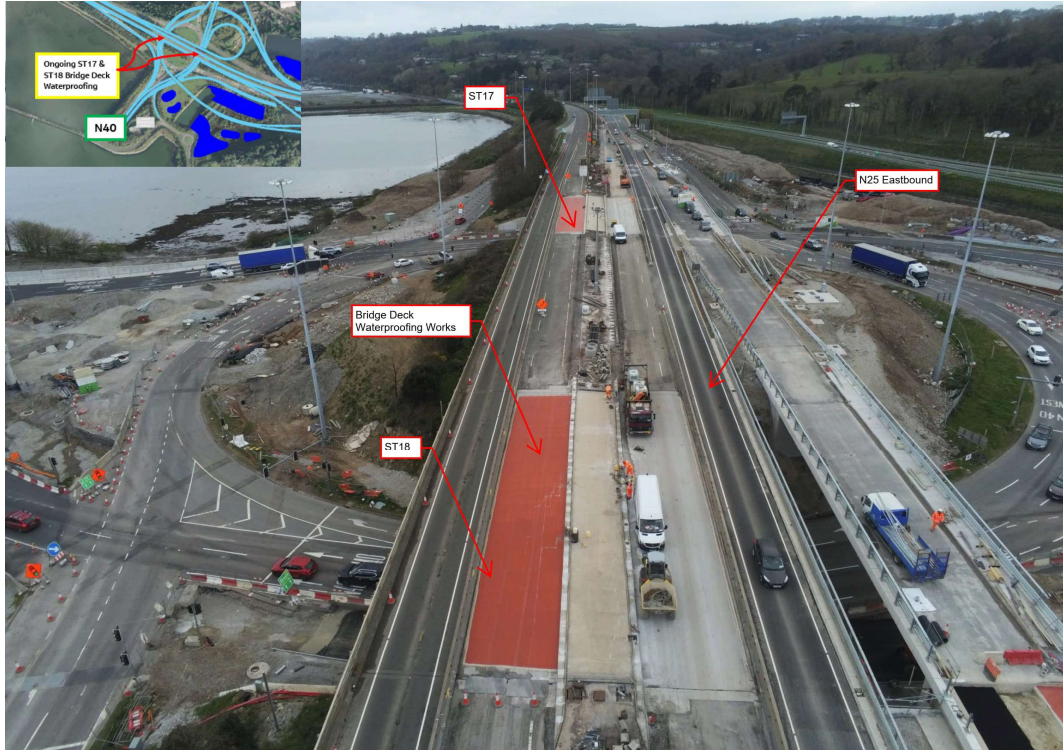


**Bridge Deck Waterproofing works areas at ST17 & ST18 within the N25 central median.**



ST17 Bridge Deck being prepared to receive waterproofing.

- Unfortunately, it will not be possible to complete bridge deck waterproofing works at Structure ST14 (see layout plan above) under lane closures. A full closure of the N25 westbound will be required for these works. We are currently targeting a closure from 7:30pm on Friday 21st April 2023 until approximately 9:00pm on Saturday 22nd April 2023. The main diversion route will be via the N40 and the southern ring road and this diversion route will be well signposted for the duration of the closure. We will confirm the dates (which will remain subject to weather conditions) in next week's update.

**This week's video shows the ongoing works in the vicinity of the Dunkettle Interchange Roundabout.**



# Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)



---

As always, if there are any queries or comments in relation to these works, please contact us at:  
**Phone:** 1800 810077 (at any time), **Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).



Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



---

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?  
You can [update your preferences](#) or [unsubscribe from this list](#).

---
