

Dunkettle Progress Update


28th April 2023



Twitter



Website

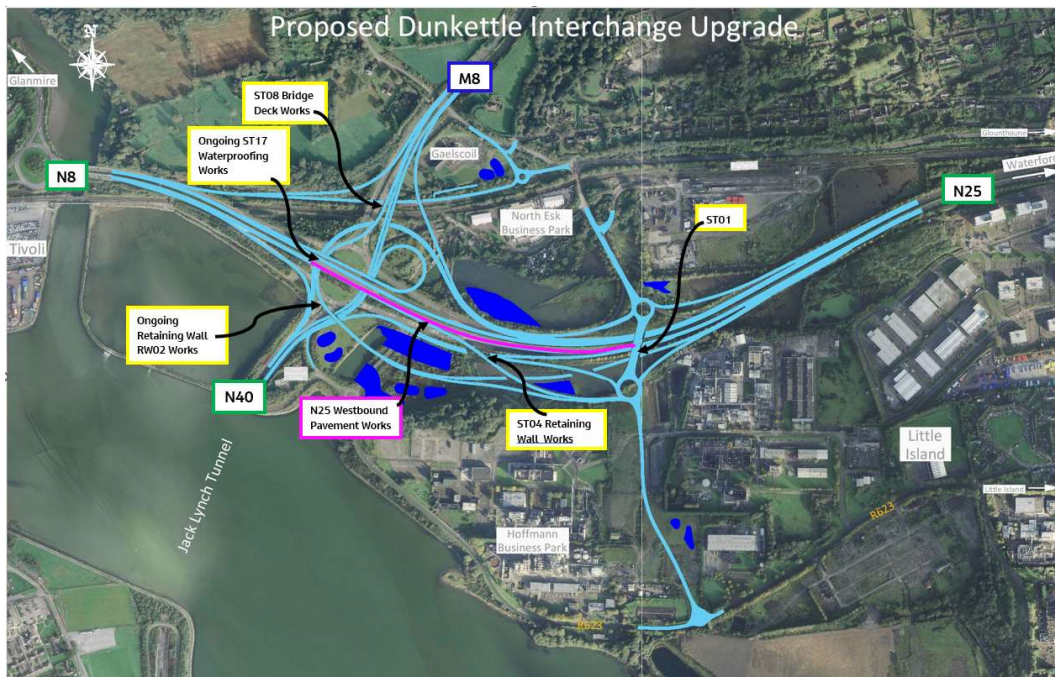


- Motorists are again reminded that speed control measures, coupled with CCTV monitoring are in place across the site and will remain in place over the coming months.

- Steel fixing for the bridge deck of Structure ST08 is ongoing at the northern side of the Interchange Roundabout alongside the M8 northbound – see photograph below.



Steel fixing works ongoing at Structure ST08

- The retaining wall at the southeast corner of Structure ST04 has been poured this week – see photograph below.

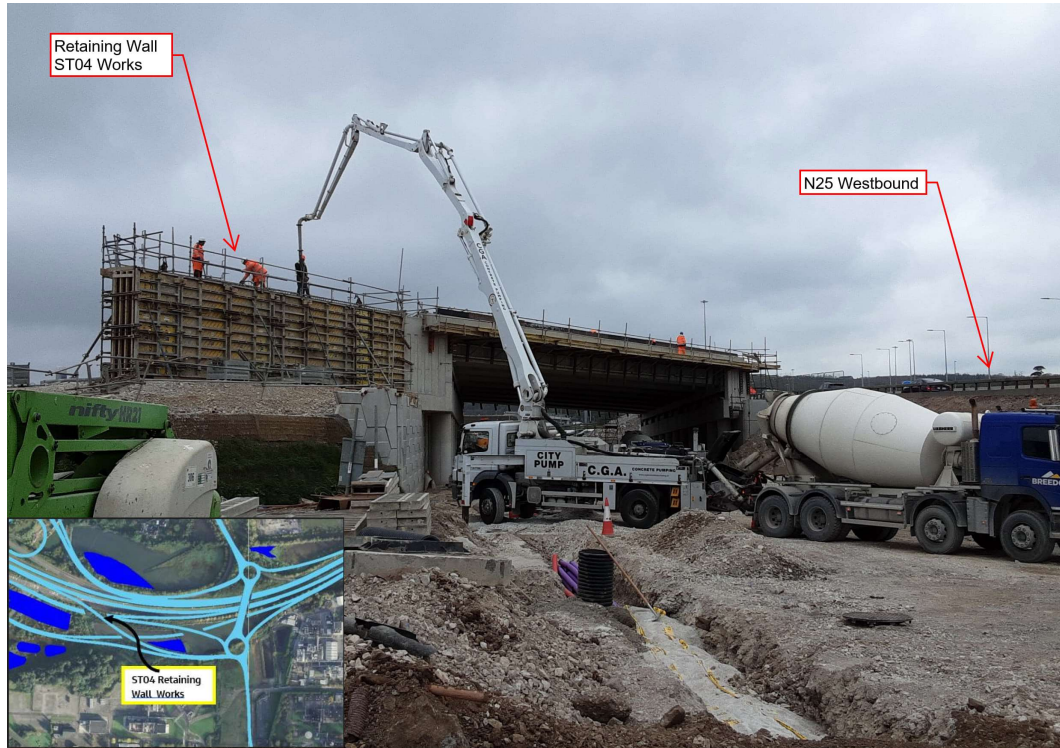

Retaining Wall pour ongoing at Structure ST04

- The reinforced soil wall, RW02, at the western side of Structure ST05 is under construction – see photograph below. Obviously, this construction will extend into the current roundabout circulatory carriageway area when this section of the roundabout is no longer required for live traffic.
- As an initial step under this heading, a minor realignment of the running lanes of the southern side of the Interchange Roundabout was progressed under night-time working last night, Thursday 27th April 2023.



Retaining Wall RW02 construction ongoing alongside the N40 at the Interchange Roundabout

- From a surfacing point of view, the focus will be on night-time working on the N25 westbound over the next week or two, starting from Tuesday 2nd May 2023. The initial works area will be between Structure ST01 and Structure ST17, the pre-existing Interchange Structure. The initial surfacing layers over the renewed bridge deck waterproofing has already been completed – see photograph below.



Installation of the sand carpet surface on top of the renewed waterproofing on Structure ST17

- In overall terms, the works remain on track for completion by the due date of February 2024.

This week's video shows the ongoing waterproofing works within the central median of the N25 overhead the Interchange Roundabout.



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:

Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.



Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
