

Dunkettle Progress Update


30th June 2023



Twitter



Website

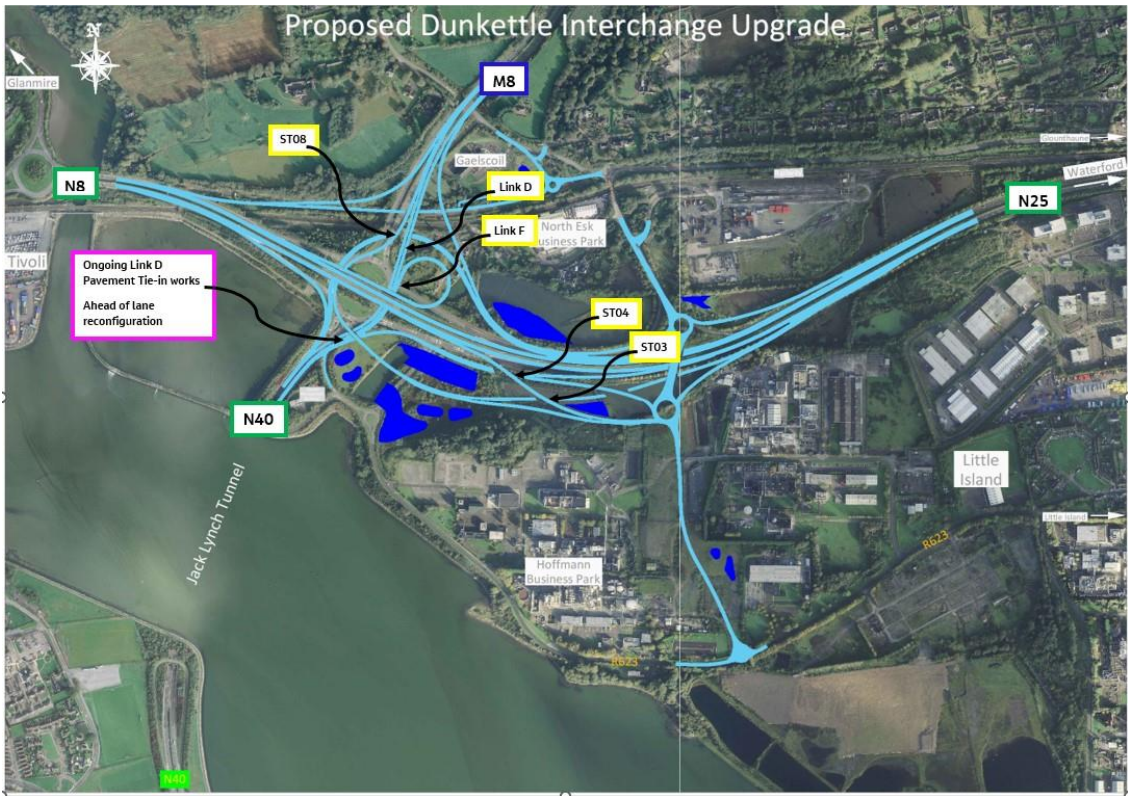


- Over the coming weeks, there will be a focus on works in online areas. Motorists are requested to pay particular attention to the posted speed limits and to note that the speed control measures will remain on site over the upcoming period.

- Surfacing works were progressed on an online section of the M8 southbound over recent days – see photograph below. The slight delay caused to M8 southbound traffic on Wednesday and Thursday was unavoidable.




Surfacing works being progressed at the M8 Southbound approach to the DKI Rdbt.

- These works will allow us to relocate the M8 Southbound traffic on the approach to the Tunnel under night time working during W/C 3rd July 2023. This will open up the majority of the remaining work areas to complete the M8 Southbound (Link D) and the N8 Eastbound (Link F) approaches to the Jack Lynch Tunnel – see photograph below.

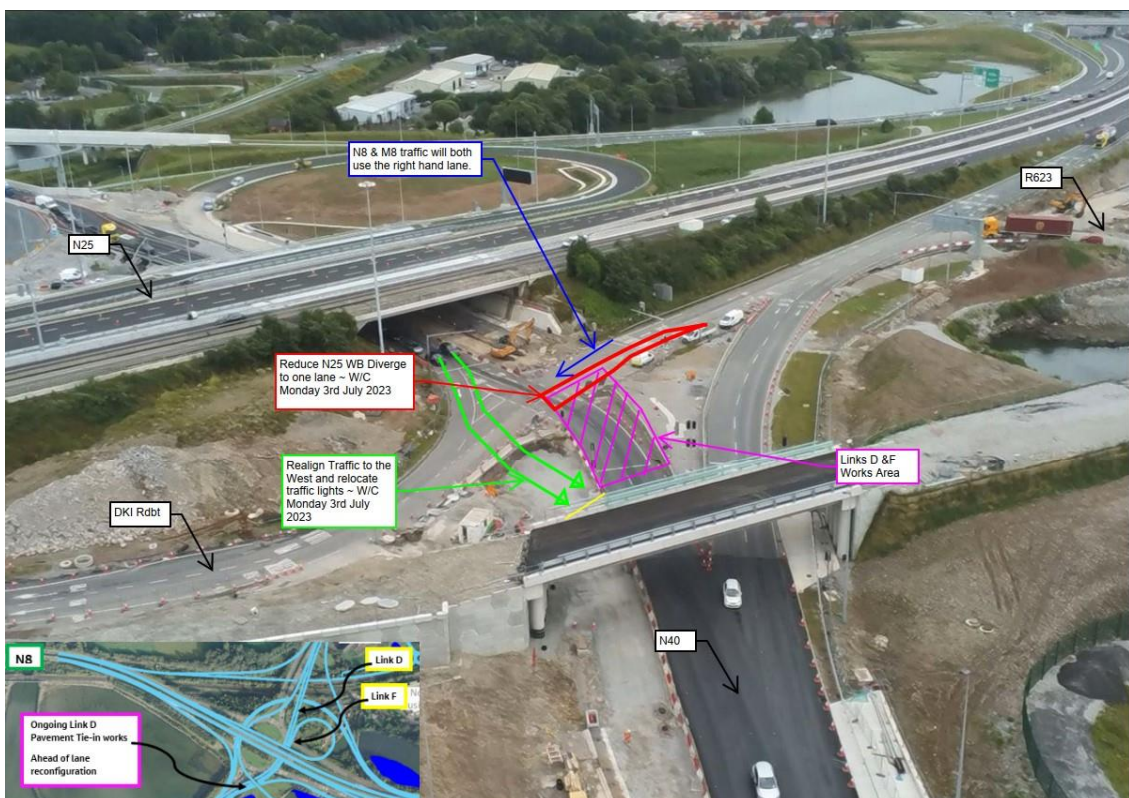


Upcoming lane reconfiguration on the M8 Southbound approach to the Tunnel.

- Today's surfacing works will be focused on Link D Northbound which will provide the new free-flow link from the Jack Lynch Tunnel to the M8 Northbound – see photograph below.

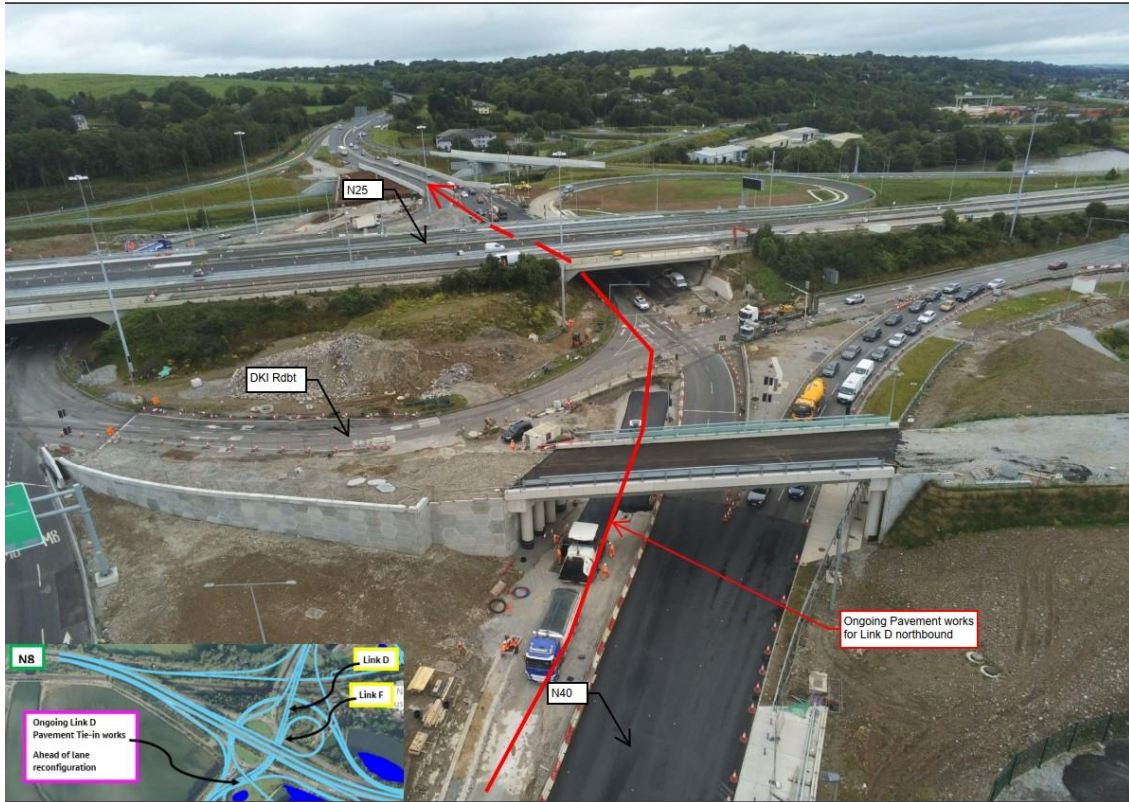


Surfacing works being progressed in the vicinity of the DK1 Rdbt. for Link D Northbound.

- From Monday 3rd July 2023, surfacing works will focus on the remaining works at Links B, F, J, K, L & M – see layout plan below.

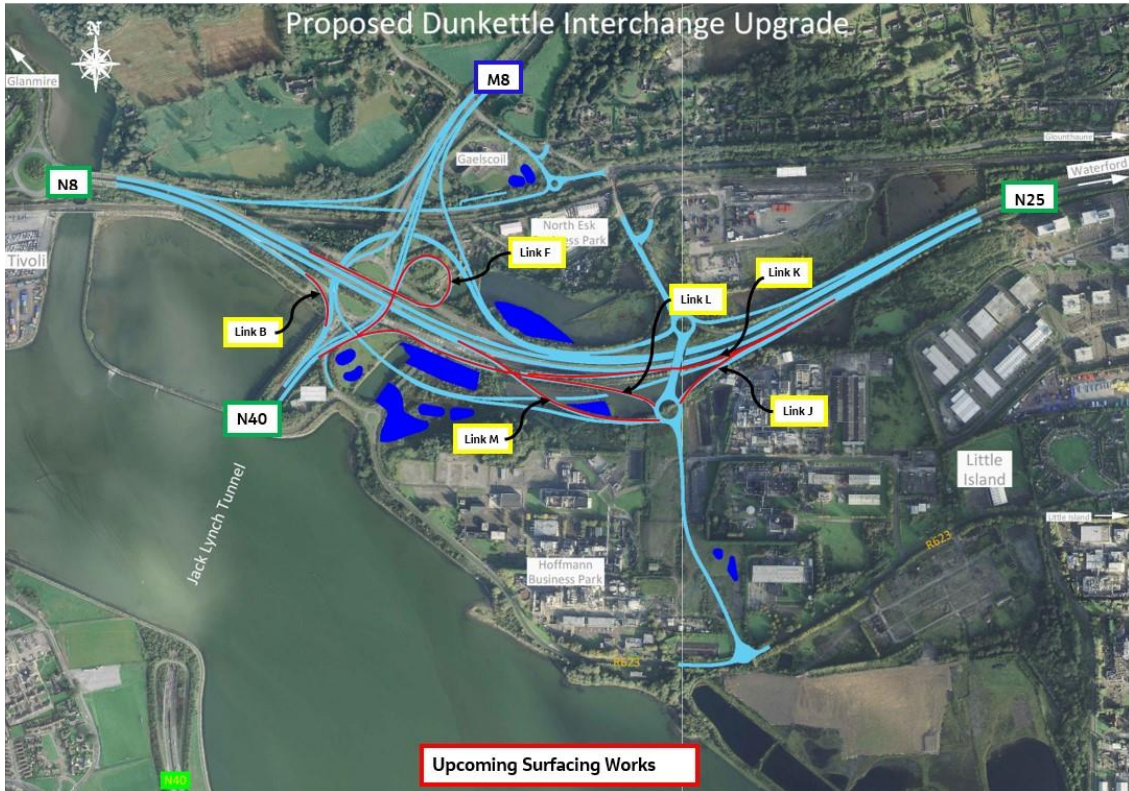

Location of the upcoming surfacing works on site.

- From a structures point of view, works on Structures ST03 and ST04 are nearing completion – see photograph below. We hope to pour the last remaining bridge deck at Structure ST08 in late July 2023 – this will be the last Structure on the project to be completed – see photograph below.

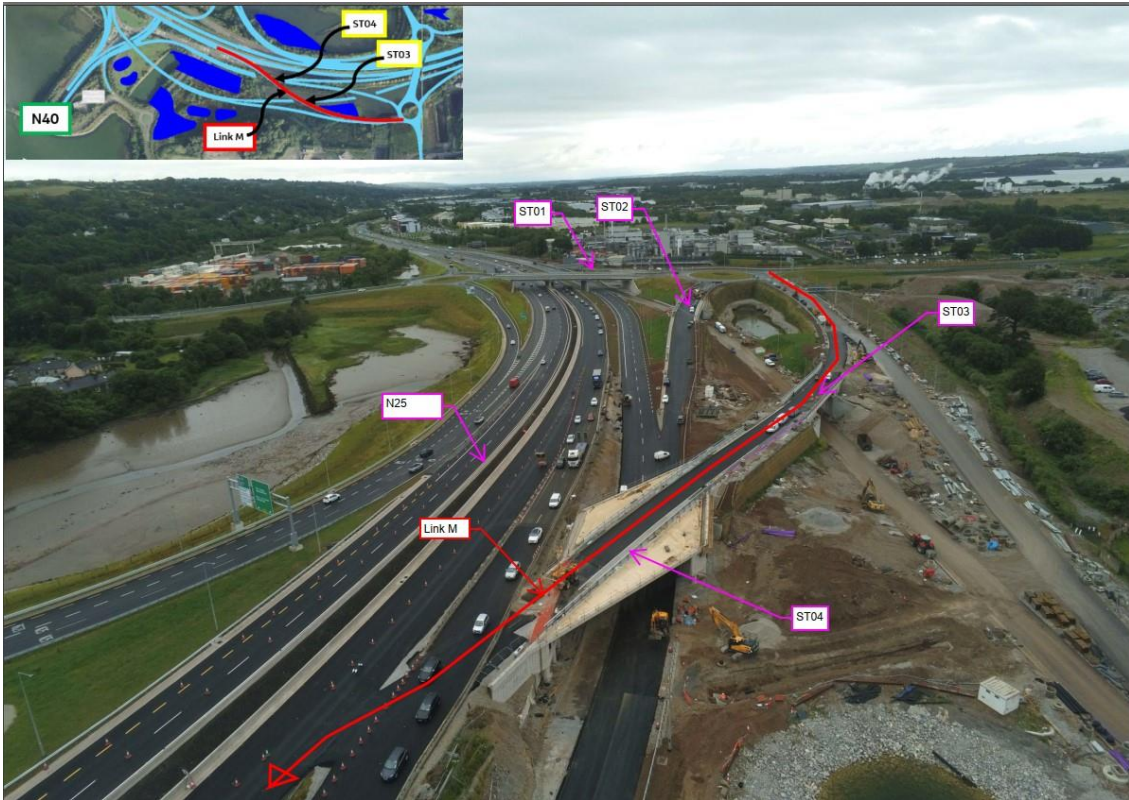

Ongoing works at Structures ST03 & ST04 alongside the N25 Westbound.



Steel fixing works ongoing at Structure ST08.

- Over the coming period we hope to open a number of further link roads – exact dates will be confirmed once they become available and additional updates will be issued setting out all relevant details of the openings themselves.

This week's Progress Update video shows the ongoing works in the vicinity of the Dunkettle Interchange Roundabout.



Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

As always, if there are any queries or comments in relation to these works, please contact us at:
Phone: 1800 810077 (at any time), **Email:** roadconstruction@ccc-site.com.

Further information on the Dunkettle Scheme can be accessed www.dunkettle.ie.

Real time traffic information can be accessed via www.dunkettletraffic.ie or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: www.dunkettle.ie/newslettersignup



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).
