



# Dunkettle Progress Update

## 06th October 2023

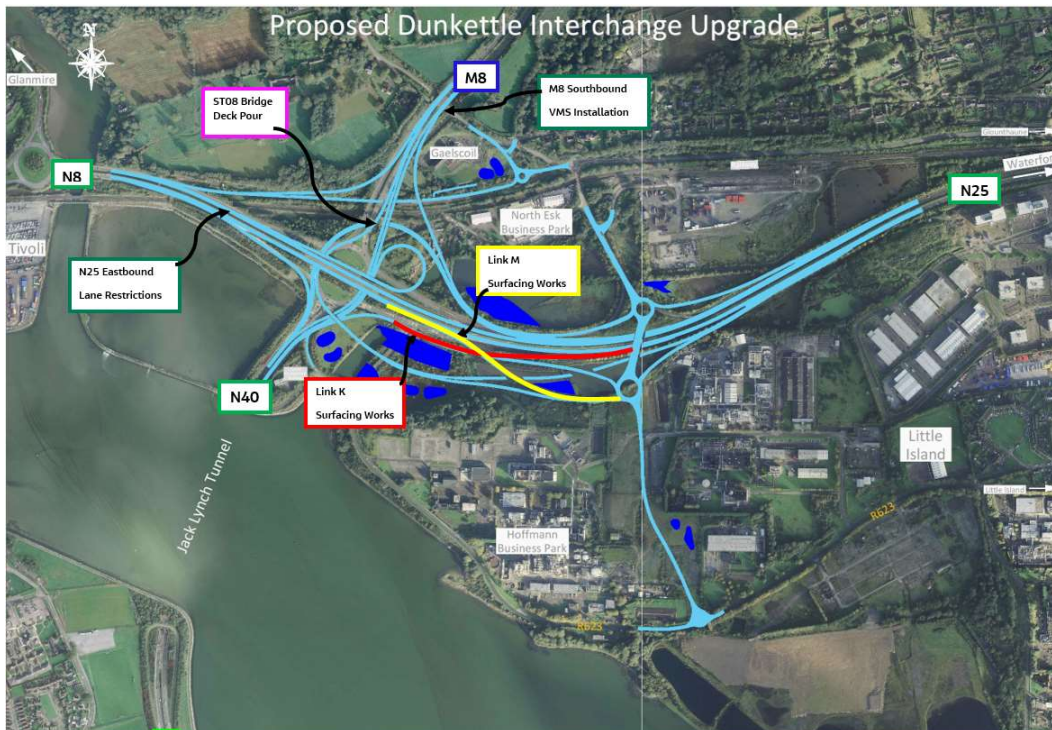


- The final bridge deck pour on the project was successfully completed on the night of Wednesday 4th October 2023 – see photograph below. We hope to complete this structure, ST08 during November 2023.

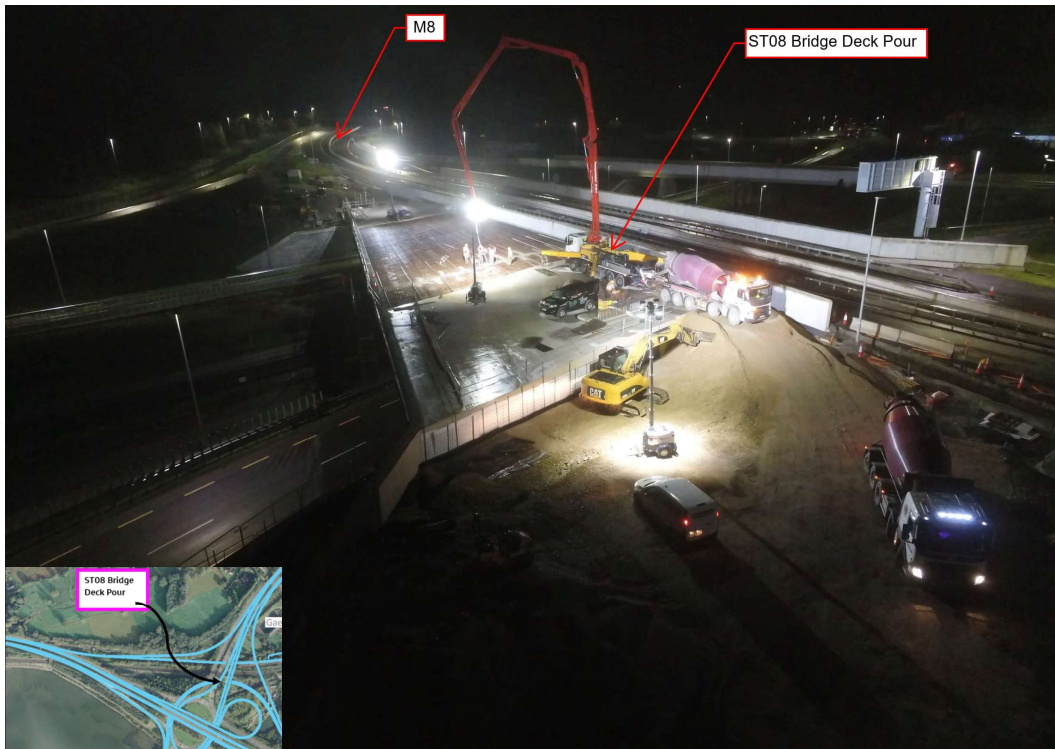

**Bridge deck concrete pour works ongoing over the Cork to Cobh Railway line at ST08**

- We hope to complete all of the N25 westbound surfacing works (see photograph below) along with the surfacing works on Link B by this coming weekend. All of the N25 westbound lanes and Link B (which caters for traffic from the tunnel looking to head west towards Cork City centre) will then be opened to their permanent alignment over the coming period.

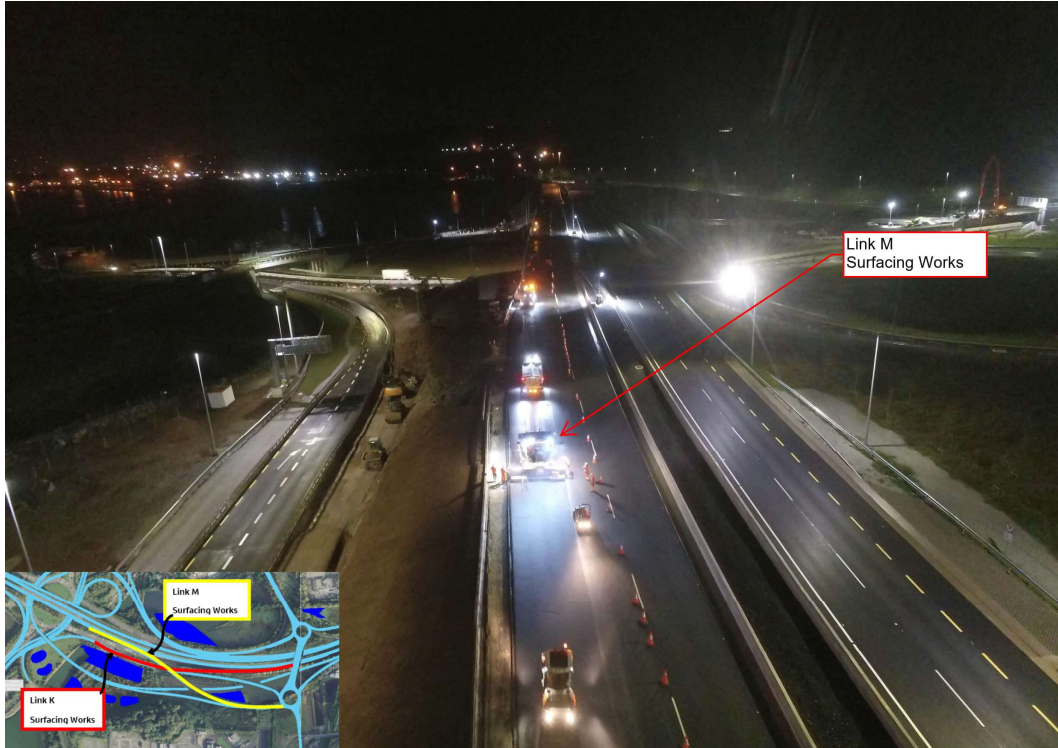

**N25 Westbound surfacing works ongoing**

- The final surfacing works on Link K should reach completion during W/C Monday 9th October 2023, with Link K then opening fully to its permanent alignment.





Surfacing works ongoing on Link K alongside the N25 Westbound

- Variable message signs have been installed on the M8 southbound and the N25 eastbound at night over the period – see photograph below. It will be necessary to bring the N25 Eastbound down to one lane from 7am to 11am on Saturday 7th October 2023 in order to progress works to the structural steel elements in advance of the remaining VMS installation works. The works are being carried out over the weekend in order to minimise the disruption to commuting traffic.



VMS installation works ongoing on the M8 southbound

**This week's Progress Update video shows the ongoing night works  
in the vicinity of the old Interchange Roundabout**



# Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)



---

As always, if there are any queries or comments in relation to these works, please contact us at:  
**Phone:** 1800 810077 (at any time), **Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).

Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



---

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?

You can [update your preferences](#) or [unsubscribe from this list](#).

---
