

# Dunkettle Progress Update


## *19th January 2024*



Twitter




Website

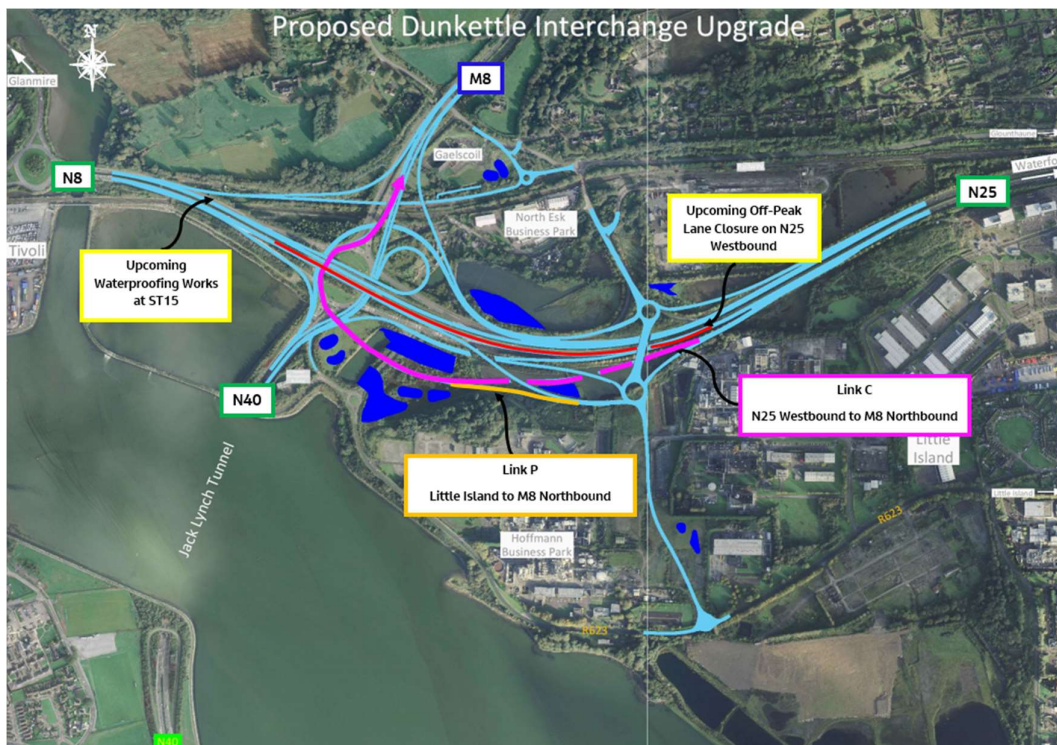

- Link C and Link P are highlighted in the layout plan above and the main works focus will be on completion of Link C over the coming weeks.

- The aerial photograph below gives an indication of the progress over recent days by comparison with the aerial photograph included in last week's update. In summary, safety barrier installation, public lighting installation, footpath construction are all progressing well and the final surfacing works required at Link C will get underway over the coming days.

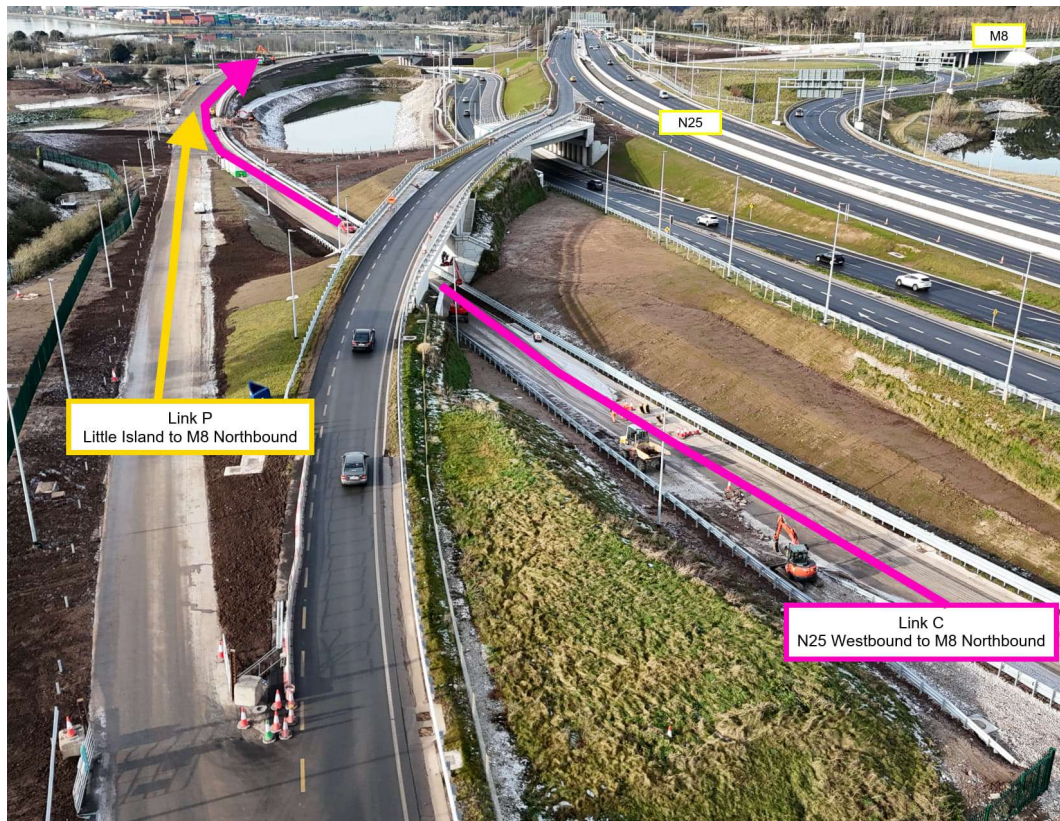

Ongoing works at Link C and Link P


- We still hope to open Link C in February 2024 with date details to follow in future Updates.

- Unfortunately, the waterproofing works required at Structure ST15 on the N25 Eastbound (see photograph below) could not be progressed this week as planned due to the extremely low temperatures over recent days. We now hope to progress these works from approximately 8pm on Thursday the 25th of January 2024 until the early afternoon of Sunday the 28th of January 2024. The N25 Eastbound will be reduced to one lane during this period and the works will be carried out on a 24-hour basis with a view to ensuring that the road reopens as planned on Sunday the 28th. These works are focused mainly on weekend working in order to minimise disruption to traffic but additional time should be allowed for journeys on this section of the N25 Eastbound during busy periods.



Area highlighted shows the extent of bridge deck waterproofing required

- Works associated with completion of expansion joints at the pre-existing Interchange bridges are scheduled for completion on Monday the 22nd of January 2024. In order to complete the works the N25 Westbound will be reduced to one lane during off peak times on Monday the 22nd in the area shown on the layout plan below.

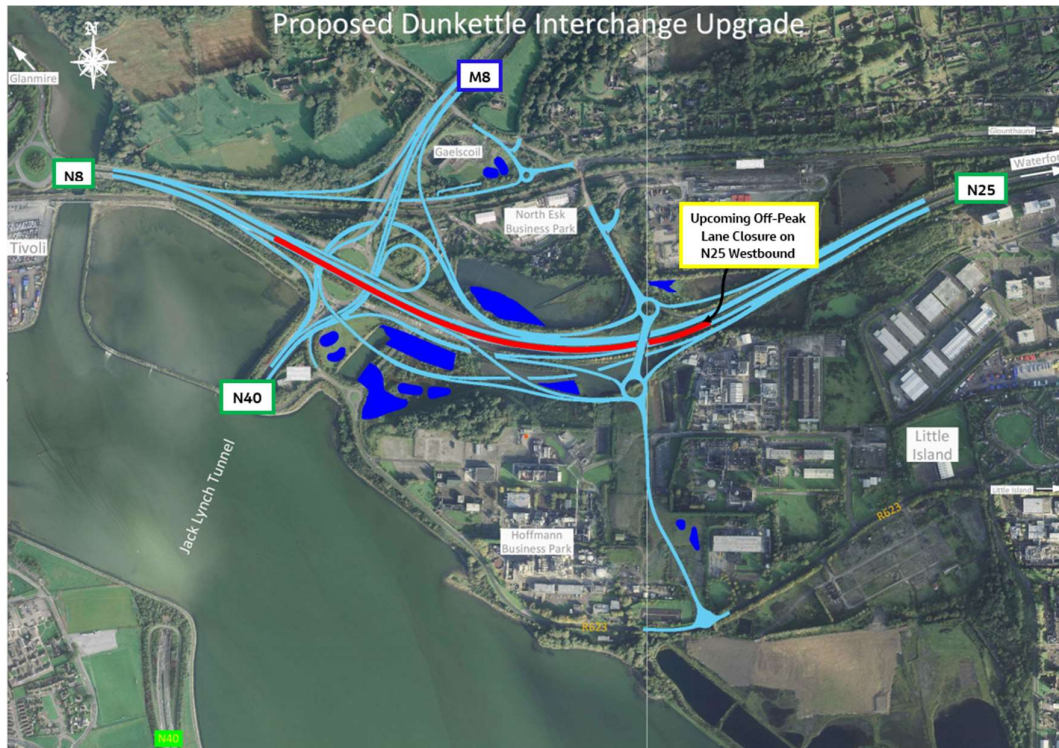

**Extent of upcoming off-peak lane closure on the N25 Westbound**

- From a programme point of view the works remain on track for the due date of February 2024

# Dunkettle Live Traffic App



Click on the icon above to see the benefits of the Dunkettle Live App.



Dunkettle Live App: Download from [Apple App store](#) or from [Google Play store](#)

---

As always, if there are any queries or comments in relation to these works, please contact us at:  
**Phone:** 1800 810077 (at any time), **Email:** [roadconstruction@ccc-site.com](mailto:roadconstruction@ccc-site.com).



Further information on the Dunkettle Scheme can be accessed [www.dunkettle.ie](http://www.dunkettle.ie).

Real time traffic information can be accessed via [www.dunkettletraffic.ie](http://www.dunkettletraffic.ie) or on the Dunkettle Live App ([Apple App store](#) and [Google Play store](#)).

New subscribers to the newsletter can register: [www.dunkettle.ie/newslettersignup](http://www.dunkettle.ie/newslettersignup)



[More at www.Dunkettle.ie](http://www.Dunkettle.ie)



---

Your email address is on a list that we use to keep you informed on the progress on the N40 and Dunkettle Interchange works.

Want to change how you receive these emails?  
You can [update your preferences](#) or [unsubscribe from this list](#).

---
